

ROYA

EXECUTIVE CONTROL TOWER

REPORT DATE: 01-AUG-2026

# ROYA-BIG PROJECT PHASE01 (B1-4)

This linked executive dashboard is generated from the platform CSV files and updates each time the platform data changes.

Schedule Health

**SPI 0.45**

Contractual Completion

**10-Apr-2027**

Forecast Completion

**19-Aug-2027**

CONTRACT VALUE

**367,286,025**  
**EGP**

Original contract value

SCHEDULE VARIANCE

**-139,711,756**  
**EGP**

EV minus PV exposure

CUMULATIVE PAID

**110,288,532**  
**EGP**

Paid to date


ONGOING RISKS

**4**

Active project constraints

PROGRESS INTELLIGENCE

# Planned vs Actual by Phase




## Critical Recovery Agenda

|                              |         |
|------------------------------|---------|
| <b>Schedule</b>              | Ongoing |
| Steel delivery delay         |         |
| Impact: High                 |         |
| <b>Schedule</b>              | Closed  |
| Deploying MEP sub contractor |         |
| Impact: High                 |         |
| <b>IFC</b>                   | Ongoing |
| IFC                          |         |
| Impact: Critical             |         |
| <b>IFC</b>                   | Ongoing |
| IFC                          |         |
| Impact: Critical             |         |
| <b>IFC</b>                   | Ongoing |
| IFC                          |         |
| Impact: Critical             |         |

PHASE GAUGES

## Plan vs Actual Snapshot



0.64%

Planned 0.98% | Variance -0.35%

0.53%

Planned 0.72% | Variance -0.19%

CONSTRUCTION

0.08%

Planned 0.44% | Variance -0.37%

OVERALL

30.68%

Planned 65.32% | Variance -34.64%

MILESTONE EXPOSURE

## Forecast Completion by Discipline / Area

| DISCIPLINE   | PLAN COMPLETION | FORECAST COMPLETION | VARIANCE DAYS |
|--------------|-----------------|---------------------|---------------|
| Engineering  | 07-Jun-2026     | 27-Feb-2027         | -265          |
| Procurement  | 16-Jan-2027     | 02-Sep-2027         | -229          |
| Construction | 05-Apr-2027     | 02-Sep-2027         | -150          |
| B-01         | 05-Apr-2027     | 05-Apr-2027         | 0             |
| B-02         | 23-Mar-2027     | 02-Sep-2027         | -163          |
| B-03         | 05-Apr-2027     | 05-Apr-2027         | 0             |
| B-04         | 05-Apr-2027     | 05-Apr-2027         | 0             |

ENGINEERING DELIVERABLES

## Document Submission Control

### Civil - Submittals

Total

Plan

Actual

193

0

0

Civil - Shop Drawings

Total  
193

Plan  
0

Actual  
0

CASHFLOW POSITION

Invoice Conversion Funnel

36.1% 36.1%  
27.8%

Submitted

INVOICES REGISTER

Payment Status Control

| PAID            |                 |
|-----------------|-----------------|
| INVOICE         | SUBMISSION DATE |
| 110,288,532 EGP |                 |
| Invoice #1      | 06-Dec-2025     |
| Invoice #2      | 29-Dec-2025     |
| Released cash   |                 |
| Invoice #3      | 24-Jan-2026     |
| Invoice #4      | 25-Feb-2026     |
| Invoice #5      | 25-Mar-2026     |

| UNDER PAYMENT          |               |
|------------------------|---------------|
| VALUE                  | STATUS        |
| 33,117,234 EGP         |               |
| 28,485,868             | Paid          |
| 26,309,020             | Paid          |
| Certified not yet paid |               |
| 20,099,944             | Paid          |
| 40,393,706             | Paid          |
| 17,641,619             | Under Payment |

INVOICE

SUBMISSION DATE

VALUE

STATUS

Invoice #6

26-Apr-2026

15,475,615

Under Payment

EARNED VALUE MANAGEMENT

## BAC / PV / EV / SV Executive Readout



## Quantitative Performance (EVM Metrics)

**CRITICAL DELAY**

BAC

**SAR**  
**367,286,024.99**

Budget @ Completion

PV

**SAR**  
**252,796,791.16**

Cumm. Planned Value

EV

**SAR**  
**113,085,034.82**

Cumm. Earned Value

SV

**SAR**  
**-139,711,756.34**

Negative schedule exposure

SPI

**0.45**

Schedule performance index

PLANNED COMPLETION VALUE POSITION

**68.8%**

PV as a share of BAC

#### EARNED VALUE GAP

# SAR

## 139,711,756.34


PV not converted into EV

#### SCHEDULE HEALTH CLASSIFICATION

# Critical Delay

Executive status

#### BAC vs PV vs EV with SV Exposure

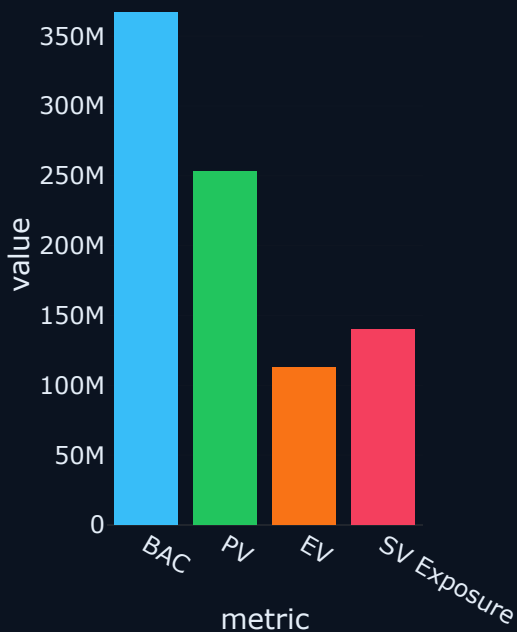

The project is underperforming against the planned value baseline. The earned value is significantly below the planned value, creating a negative schedule variance of SAR 139.71M and an SPI of 0.45. This indicates that the project is progressing at approximately 45% of the planned schedule efficiency.

**ADD / EDIT MY COMMENT**

No user comment added.

# Root Cause Linkage

| Cause Title                                                  | Impact Area                              | Link to EVM Impact                                                                                                   | Status  | Severity |
|--------------------------------------------------------------|------------------------------------------|----------------------------------------------------------------------------------------------------------------------|---------|----------|
| Delay in RFT steel supply by Owner                           | Procurement / Construction               | PV not converted into EV due to blocked work fronts and delayed material-driven execution.                           | Ongoing | Critical |
| Delay in design review process                               | Engineering                              | Planned engineering progress could not flow into approved deliverables and downstream earned value.                  | Closed  | High     |
| Delay in reply on RFI 4 and RFI 5                            | Engineering / Construction               | Technical closure delays restricted workface release and slowed conversion of planned progress into earned progress. | Ongoing | High     |
| Delay in determining the MEP executing party                 | Engineering / Procurement / Construction | Interface uncertainty delayed execution planning, procurement flow, and forecast progress realization.               | Closed  | Medium   |
| Payment delay impact on resource continuity and productivity | Commercial / Construction                | Liquidity pressure reduced productivity continuity and slowed the conversion of planned value into earned value.     | Ongoing | High     |

The negative schedule variance is not an isolated numerical deviation. It is directly linked to unresolved external and interface-driven constraints that prevented planned progress from being converted into earned value, mainly within construction and procurement work fronts.

**ADD / EDIT MY COMMENT**

No user comment added.

# Contractor Mitigation & Recovery Status

| ACTION                             | OWNER / RESPONSIBLE PARTY                        | CURRENT STATUS                | RECOVERY IMPACT                                                                     | REQUIRED NEXT DECISION                                                  |
|------------------------------------|--------------------------------------------------|-------------------------------|-------------------------------------------------------------------------------------|-------------------------------------------------------------------------|
| RFT Steel Supply Recovery          | Project Controls / Procurement / Owner Interface | In Progress                   | Releases blocked structural work fronts and supports EV generation in construction. | Secure committed steel release and delivery sequence from Owner.        |
| RFI Closure Acceleration           | Engineering Team / Consultant Interface          | In Progress                   | Enables technical closure and unblocks affected planned activities.                 | Escalate overdue RFI responses for closure dates.                       |
| Design Review Follow-up            | Engineering Management                           | Monitoring                    | Protects planned engineering completion and downstream procurement readiness.       | Freeze review turnaround commitments with reviewing parties.            |
| MEP Interface Finalization         | Project Management / Client Interface            | Monitoring                    | Reduces interface uncertainty and improves forecast execution reliability.          | Confirm final executing responsibility and interface release logic.     |
| Commercial / Payment Follow-up     | Commercial Team                                  | In Progress                   | Supports resource continuity and mitigates productivity disruption risk.            | Close outstanding payment approvals and release under-payment invoices. |
| Construction Productivity Recovery | Construction Team                                | Ready Upon Constraint Removal | Accelerates EV generation once technical and supply constraints are removed.        | Approve recovery sequence by priority work front.                       |

Contractor mitigation is focused on protecting available work fronts, accelerating technical closures, maintaining commercial entitlement records, and recovering productivity once external constraints are removed. Recovery remains dependent on timely closure of outstanding Owner / Engineer-driven constraints.



**ADD / EDIT MY COMMENT**

No user comment added.

RISK REGISTER

## Risk & Issue Control

### Schedule

Ongoing

Steel delivery delay

Impact: High

### Schedule

Closed

Deploying MEP sub contractor

Impact: High

### IFC

Ongoing

IFC

Impact: Critical

### IFC

Ongoing

IFC

Impact: Critical

### IFC

Ongoing

IFC

Impact: Critical

CAUSAL INTELLIGENCE

## Root Cause / Impact Radar

Root Cause / Impact Radar

# RFT Quantity Distribution

No dedicated resource quantity source is currently available.

Effective Date: 11-Sep-2025 *Æ'çâ,¬Å¡fâ€šÅ,Å* Ground Works Forecast: 11-Sep-2025

Strategic priority: recover construction productivity and preserve entitlement evidence.
