

Ref No.: BD-ACEPM-SAMCO-LET-040

Date: Tuesday, 07th of July 2026

To: SAMCO National Construction Company
Attention: Eng. Mohammed Sami Mohammed (Project Manager)

Project Name: The Big Business District
Contract/Package: Construction Works of the Civil Works for Buildings B1, B2, B3 and B4

Subject: Notice of Slow Progress Rate and Comments on Monthly Progress Report – June 2026

Reference (S):

- 1) Contractor's Monthly Report Ref. BD-CW-Samco-ACE-Ds-Gen-0016 dated 30/06/2026

Dear Sir,

With reference to the above-mentioned subject and the Contractual obligations stipulated in the signed Contract and the Monthly Report Ref. no. 1, the Engineer formally expresses its concern regarding the Contractor's inability to maintain the required progress in executing critical Project activities, as set forth in the approved Programme.

It has become apparent that the Contractor has failed to meet the performance expectations established under the approved Programme, as evidenced by the latest project performance evaluation and the recorded Schedule Performance Index (SPI) of 0.49, which reflects a significant delay in the progress of the Works compared to the planned schedule. Furthermore, Building No. 4 has recorded no progress due to the ongoing tank injection works, which must be completed without further delay to enable the continuation and completion of Building No. 4 and avoid any additional impact on the Project schedule. The current delay is attributable to the Contractor's slow progress in executing the Works and its failure to undertake the necessary measures to expedite the affected activities and recover the delay.

These indicators clearly reflect the ongoing delay in executing the Project activities, causing a significant deviation from the approved Programme. This deficiency is impeding the overall progress of the Works and poses a serious risk of further slippage in the Contractual Time for Completion.

On the other hand, Attachment No. (01) includes all comments related to the previously submitted Monthly Report for June 2026. Accordingly, the Contractor is hereby requested to address the mentioned comments, amend the report accordingly, and resubmit the revised version for further necessary action.

In light of the above, and in accordance to Sub Clauses 3.3[Instructions of the Engineer], 8.3 [Programme] and 8.6 [Rate of Progress] of the contract, the Contractor is requested to exert its utmost endeavors to recover the accrued delay by taking immediate corrective action to improve its performance through the proper allocation of resources, avoid any negative impact on the overall project timeline, and provide a detailed report outlining the mitigation measures adopted to expedite project progress and effectively address these delays.



CE Project Management | ACE Group
12 Makram Ebied st. -Nasr City - Cairo
Nasr City, Cairo, Egypt
Tel : + 202 2273 8566
Tel : + 202 7385 4677
E-mail: ace.ho@ace-mb.com



The Engineer hereby notifies the Contractor that it shall be held liable for consequences resulting from non-compliance with the above.



Attachment(s):

1. Comments on Monthly Report May 2026

CC:

Eng. Mostafa Galal - Owner representative
Eng. Ahmed Saafan – Project Controls Director
Eng. Ramy Refaat – Commercial Contracts Director
Eng. Osama Waly – PCO representative

M.S

ACE-PM Monthly Review Report – June.2026

- General:**



- On page 4, under “Project Key Contractual Milestones”:


Milestones	Contract Dates
Project Start Date	11-Sep-25
Contract Award	11-Sep-25
IFC Drawing Package	11-Sep-25
Ground works finish date	11-May-26
Project finish date	10-Apr-27

- Based on the submitted XER file (The Project finish date: 5-Sep-2027):

Key Dates		725	0%	11-Sep-25 A	05-Sep-27
Milestone		725	0%	11-Sep-25 A	05-Sep-27
KD-MS-1000	Project Start Date	0	100%	11-Sep-25 A	
KD-MS-1010	Contract Agreement	0	100%	11-Sep-25 A	
KD-MS-1020	IFC Drawing Package	0	100%	11-Sep-25 A	
KD-MS-1040	Ground Works Finish Date	0	0%		08-Oct-26*
KD-MS-1050	Project Finish Date	0	0%		05-Sep-27*

- On page 7 and 8, under “Progress Status for Each Building”:

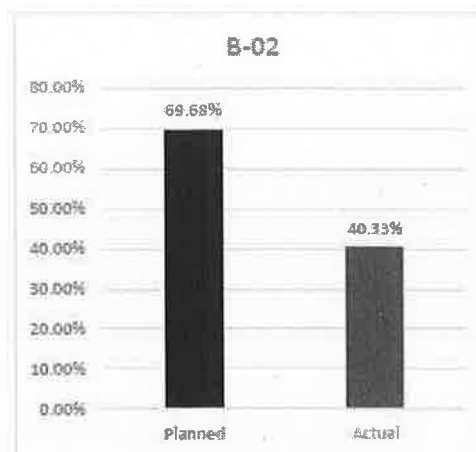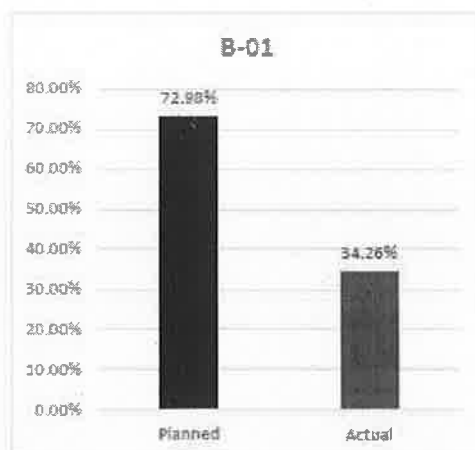

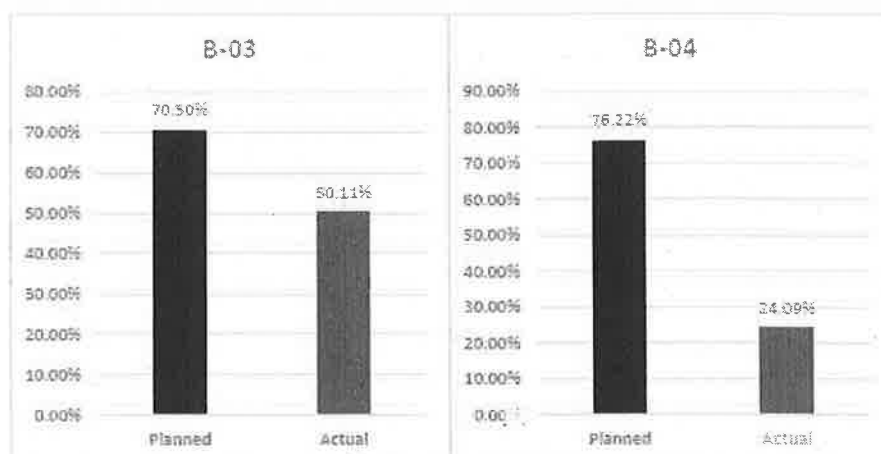

Conclusion:

- 1- Building 1 is behind schedule by 147 days delay
- 2- Building 2 is behind schedule by 132 days delay
- 3- Building 3 is behind schedule by 128 days delay
- 4- Building 4 is behind schedule by 149 days delay

- Based on the submitted XER file:

Building B01	721	35.7%	11-Sep-25 A	01-Sep-27	73.57%	11-Sep-25	07-Apr-27	-147
Building B02	687	41.77%	11-Sep-25 A	29-Jul-27	70.41%	11-Sep-25	23-Mar-27	-115
Building B03	681	51.3%	27-Sep-25 A	08-Aug-27	71.21%	27-Sep-25	05-Apr-27	-123
Building B04	713	25.31%	21-Sep-25 A	03-Sep-27	76.6%	13-Sep-25	07-Apr-27	-149

- The Contractor shall take into consideration the earthworks activities when calculating the actual and planned progress percentages.

3. Out-of-sequence activities:

CON-B03-BAS01-1000	Scaffolding works for Walls, Col. & Cores (B03) (Bas 01)
CON-B03-BAS01-1010	RFT for Walls, Col. & Cores (B03) (Bas 01)
CON-B03-BAS01-1020	Shuttering for Walls, Col. & Cores (B03) (Bas 01)
CON-B03-BAS01-1030	Pouring for Walls, Col. & Cores (B03) (Bas 01)
CON-B03-BAS01-1040	Shuttering for Slabs & Beams (B03) (Bas 01)

4. Activities with Actual Dates > Data Date

E-SUB-B03-1ST-1030	Submittal for Slabs Conc. Dim. & RFT DWGs (B03) (1st)
--------------------	---

5. The Contractor shall verify the reported progress percentages in line with the actual site status.
6. The number of critical activities is **563** out of 1,363 (**41.3%**), which indicates an increased level of project risk.

- **Conclusion:**

1. Building.04 has made **no progress** due to the ongoing tank injection works, The tank works must be completed as soon as possible to allow the completion of B.04 and prevent any further delays.
2. The delay is attributable to the contractor's slow progress in executing the works.
3. The Contractor shall do his utmost to mitigate the project delays.
