

Ref No.: BD-CW-SAMCO-ACE-LET-STR-046

24-January-2026

To: ACE Project Management | Moharram Bakhoun

Attention: Eng. Abdulaziz Mohamed (Project Manager)

Project Name: The Big Business District.

Contract/Package: Construction Works of the Civil Works for Buildings B1, B2, B3 and B4 – Phase 1.

Subject: Submission of Interim Payment Certificate No. 3

Dear Sir,

With reference to the above-mentioned subject, we hereby submit **Interim Payment Certificate No. 3** for your review and approval.

The submission includes both **soft and hard copies** of the certificate as required.

Attached:

– Interim Payment Certificate No. 3 (Soft & Hard Copies)

Best regards,

Eng./ Mohammed Sami Mohammed
Project Director
SAMCO National Construction



بتاريخ: 2026 /02/10

المرجع : BD-ACEPM-ROYA-LET-011

السادة : شركة رؤية للإستثمار العقاري
عنـاية : المهندس / مصطفى جلال

اسم المشروع : The BIG

اسم العقد : The BIG -SAMCO

الموضوع : توصيات الخاصة بشأن مستخلص رقم 3- شركة سامكو الوطنية للإنشاءات

تحية طيبة وبعد،،،

بالإشارة الى الموضوع المذكور أعلاه ، مرفق طيه المستخلص الجاري رقم (3) لمشروع The Big (شركة سامكو الوطنية للإنشاءات) ، عن الأعمال المنفذه حتي تاريخ 2026-01-20 وتمت مراجعته فنيا بقيمه اجمالية (79,680,101.10) جنيه مصري (تسعة و سبعون مليون و ستمائة و ثمانون ألف و مائة و واحد جنيه مصري و عشرة قرش لا غير) شاملا ضريبة القيمة المضافة وقد تمت مراجعة المستخلص فنيا وتعاقديا ولا مانع من صرف قيمة المستخلص مع : راعاه ما يلي

1. تطبيق بنود التعاقد

2.مراجعة ما سبق صرفه

وتفضلوا بقبول فائق الاحترام والتقدير...



Ref No.: BD-ACEPM-ROYA-LET-0011

10th of February 2026

To: Roya Developments

Attention: Eng.: Mostafa Galal

Project: The BIG

Package: Construction Works of the Civil Works for Buildings B1, B2, B3 and B4 (The Big)

Subject: ACEPM Recommendation of Monthly Interim Payment No. (3) SAMCO Al-Watanya for Construction

Dear Sir

With reference to the a/m subject, ACEPM hereby draws Roya Development's kind attention to the recommendation made by ACEPM for the Contractor's Interim Payment No.2 with the cut-off date of 20RD January 2026 submitted via letter dated 25th January 2026 as follows:

- The Interim Payment was reviewed by ACE (from a technical point of view) and its assessment was sent to ACEPM via TR NO.0058 dated Thursday, 22th of January 2026,
- ACEPM recommendation for the amount due to the Contractor (recommendations of the related Interim Payment Certificate "IPC") is shown in the following table based on the attached supporting particulars: -

Submissions	Gross Amount of Invoice			Net Amount of Invoice		
	Previous	Current	Total	Previous	Current	Total
Contractor's First Submission	56,766,164.94	29,327,167.05	86,093,331.99	38,810,424.59	23,841,979.73	62,652,404.32
Contractor's Second Submission	N/A	N/A	N/A	N/A	N/A	N/A
ACEPM's Recommendations	56,766,164.94	22,913,936.16	79,680,101.10	38,810,424.59	11,540,721.07	50,351,145.66

- An amount of (4,134,485) EGP. has been deducted from the work certified due to non-submission from SAMCO of the BOQ breakdown,

Yours faithfully

Eng./ Abdelaziz Mohamed



Attachments: As Enclosed.

Project Information			
Project Name	The big	The Accepted Contract Amount	367,286,025
Employer	ROYA	Contractor name/scope	Samco Al-Wataniya for Construction
Engineer	ACE CONSULTANT	Cut of Date	January 20/2026
Project Manager	ACE project Management	IPC No	3
		Contract Start Date	11-Sep-25
Contract Type /NO	Roya-Big-2025-01	Contract End Date	10-Apr-27

Contractual Terms		
	Item	Amount
A	Accepted Contract Amount	367,286,025.00
B	Accepted variation Amount	
D= Revised Contract Sum " A + B " =		367,286,025.00

Advance payment conditions		
	Item	Amount
A	Advanced Payment	91,821,506.25
B	Recovery for Advanced Payment	17,473,706.38
C= Advanced Payment Balance " A + B " =		74,347,799.87

Payment Details		A	B = C - A	C
		Previous Work Certified	Current Amount	Work Certified To-Date
A-	Certified steel Work Volume of Accepted contract	34,455,374.54	20,099,944.00	54,555,318.54
B-	Certified Work Volume of Variation Order	15,339,506.99		15,339,506.99
C-	Certified Price Variance			
E= Total Work Certified excluding VAT " A + B + C " =		49,794,881.53	20,099,944.00	69,894,825.53
F=VAT		6,971,283.41	2,813,992.16	9,785,275.57
G=Total Work Certified including VAT " E + F " =		56,766,164.94	22,913,936.16	79,680,101.10

H= Material on site				
Deductions:				
J=E*(x%)	Retention 5%	2,489,744.08	1,004,997.20	3,494,741.28
K=E*(x%)	Advance payment 25%	12,448,720.38	5,024,986.00	17,473,706.38
L=E*(x%)	Withholding Tax 1.00%	497,948.82	200,999.44	698,948.26
M=E*(x%)	Social Insurance 5.00%	2,489,744.08	1,004,997.20	3,494,741.28
N	Other Deductions/back charges	29,583.00	2,750.00	32,333.00
N'=VAT Retention Amount			4,134,485.25	4,134,485.25
O =Total Deductions= sum (J:N) =		17,955,740.35	11,373,215.09	29,328,955.44
P=Total due amounts " G + H -O " =		38,810,424.59	11,540,721.07	50,351,145.66

Previous paid				
Current Net Payment				50,351,145.66
Amounts in words		Fifty million Three hundred fifty-one thousand one hundred forty-five Egyptian pounds and sixty-six piastres only.		

Certifications:			
The Contractor		The Consultant	
Project Manager	Technical Office manager	Project Manager	Cost Control manager
Name:	Name:	Name:	Name:
Signature:	Signature:	Signature:	Signature:
Date:	Date:	Date:	Date:
The Project Manager		The Employer	
Project Manager	Cost Control manager	Project Manager	Commercial Director
Name:	Name:	Name:	Name:
Signature:	Signature:	Signature:	Signature:
Date:	Date:	Date:	Date:

Project Information

Project Name	The big	The Accepted Contract Amount	367,286,025
Employer	ROYA	Contractor name/scope	Samco Al-Wataniya for Construction
Engineer	ACE CONSULTANT	Cut of Date	January 20/2026
Project Manager	ACE project Management	IPC No	3
		Contract Start Date	11-Sep-25
Contract Type /NO	Roya-Big-2025-01	Contract End Date	10-Apr-27

Contractual Terms

	Item	Amount
A	Accepted Contract Amount	367,286,025.00
B	Accepted variation Amount	
D= Revised Contract Sum " A + B " =		367,286,025.00

Advance payment conditions

	Item	Amount
A	Advanced Payment	91,821,506.25
B	Recovery for Advanced Payment	17,473,706.38
C= Advanced Payment Balance " A + B " =		74,347,799.87

Payment Details		A	B = C - A	C
		Previous Work Certified	Current Amount	Work Certified To-Date
A-	Certified steel Work Volume of Accepted contract	34,455,374.54	20,099,944.00	54,555,318.54
B-	Certified Work Volume of Variation Order	15,339,506.99	-	15,339,506.99
C-	Certified Price Variance	-	-	-
E= Total Work Certified excluding VAT " A + B + C " =		49,794,881.53	20,099,944.00	69,894,825.53
F=VAT		6,971,283.41	2,813,992.16	9,785,275.57
G=Total Work Certified including VAT " E + F " =		56,766,164.94	22,913,936.16	79,680,101.10

H= Material on site

Deductions:

J=E*(x%)	Retention	5%	2,489,744.08	1,004,997.20	3,494,741.28
K=E*(x%)	Advance payment	25%	12,448,720.38	5,024,986.00	17,473,706.38
L=E*(x%)	Withholding Tax	1.00%	497,948.82	200,999.44	698,948.26
M=E*(x%)	Social Insurance	5.00%	2,489,744.08	1,004,997.20	3,494,741.28
N	Other Deductions/back charges		29,583.00	2,750.00	32,333.00
N*=VAT Retention Amount			-	4,134,485.25	4,134,485.25
O =Total Deductions= sum (J:N*) =			17,955,740.35	11,373,215.09	29,328,955.44

P=Total due amounts " G + H - O " =

		38,810,424.59	11,540,721.07	50,351,145.66
--	--	---------------	---------------	---------------

Previous paid

Current Net Payment	50,351,145.66
---------------------	---------------

Amounts in words

Fifty million Three hundred fifty-one thousand one hundred forty-five Egyptian pounds and sixty-six plasters only.

Certifications:

The Contractor

Project Manager

Name:

Signature:

Date:

Technical Office manager

Name:

Signature:

Date:

Cost Control Engineer

Name:

Signature:

Date:

The Consultant

Project Manager

Name:

Signature:

Date:

Cost Control manager

Name:

Signature:

Date:

Cost Control Engineer

Name:

Signature:

Date:

The Project Manager

Project Manager

Name:

Signature:

Date:

Cost Control manager

Name:

Signature:

Date:

The Employer

Project Manager

Name:

Signature:

Date:

Commercial Director

Name:

Signature:

Date:

Cost Control Manager

Name:

Signature:

Date:



367286025.00	البيانات العامة	The Big	اسم المشروع
Samco Al-Wataniya for Construction	المقر	ROYA	المالك
January 20/2026	اصال حتى	ACE CONSULTANT	الاستشاري
3	رقم المستخلص	ACE project Management	مدير المشروع
11-Sep-25	تاريخ بدء العقد		
10-Apr-27	تاريخ انتهاء العقد	Roya-Big-2025-01	نوع العقد / رقم

البيانات العامة	البيانات العامة	البيانات العامة
قيمة	قيمة	قيمة
367,286,025.00	A قيمة العقد	
	B قيمة اموال العميل	
367,286,025.00	D = A + B =	

البيانات العامة	البيانات العامة	البيانات العامة
قيمة	قيمة	قيمة
91,821,506.25	A قيمة العقد	
17,473,706.38	B قيمة اموال العميل	
74,347,799.87	C = A + B =	

C	B = C - A	A	البيانات العامة
البيانات العامة	قيمة اموال العميل	قيمة اموال العميل	
54,555,318.54	20,099,944.00	34,455,374.54	A - قيمة اموال العميل
15,339,506.99		15,339,506.99	B - قيمة اموال العميل
			C - قيمة اموال العميل
69,894,825.53	20,099,944.00	49,794,881.53	E = A + B + C =
9,785,275.57	2,813,992.16	6,971,283.41	F = قيمة اموال العميل
79,680,101.10	22,913,936.16	56,766,164.94	G = E + F =
			H = قيمة اموال العميل

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
3,494,741.28	1,004,997.20	2,489,744.08	5%
17,473,706.38	5,024,986.00	12,448,720.38	25%
698,948.26	200,999.44	497,948.82	1.00%
3,494,741.28	1,004,997.20	2,489,744.08	5.00%
32,333.00	2,750.00	29,583.00	N
4,134,485.25	4,134,485.25	0.00	N
29,328,955.44	7,238,729.84	17,955,740.35	O = sum (J-N) =
50,351,145.66	15,675,206.32	38,810,424.59	P = G + H - O =
50,351,145.66			

Certifications:	The Contractor	The Consultant	The Employer
Project Manager	Project Manager	Project Manager	Project Manager
Name:	Name:	Name:	Name:
Signature:	Signature:	Signature:	Signature:
Date:	Date:	Date:	Date:
Cost Control manager	Cost Control manager	Cost Control manager	Cost Control manager
Name:	Name:	Name:	Name:
Signature:	Signature:	Signature:	Signature:
Date:	Date:	Date:	Date:
Commercial Director	Commercial Director	Commercial Director	Commercial Director
Name:	Name:	Name:	Name:
Signature:	Signature:	Signature:	Signature:
Date:	Date:	Date:	Date:

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
367286025.00	البيانات العامة	The Big	البيانات العامة
Samco Al-Wataniya for Construction	البيانات العامة	ROYA	البيانات العامة
January 20/2026	البيانات العامة	ACE CONSULTANT	البيانات العامة
3	البيانات العامة	ACE project Management	البيانات العامة
11-Sep-25	البيانات العامة	Roya-Big-2025-01	البيانات العامة
10-Apr-27	البيانات العامة		البيانات العامة

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
367,286,025.00	البيانات العامة	A	البيانات العامة
	البيانات العامة	B	البيانات العامة
367,286,025.00	البيانات العامة	D = A + B =	البيانات العامة

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
91,821,506.25	البيانات العامة	A	البيانات العامة
17,473,706.38	البيانات العامة	B	البيانات العامة
74,347,799.87	البيانات العامة	C = A + B =	البيانات العامة

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
54,555,318.54	البيانات العامة	34,455,374.54	البيانات العامة
15,339,506.99	البيانات العامة	15,339,506.99	البيانات العامة
69,894,825.53	البيانات العامة	49,794,881.53	البيانات العامة
9,785,275.57	البيانات العامة	6,971,283.41	البيانات العامة
79,680,101.10	البيانات العامة	56,766,164.94	البيانات العامة

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
	البيانات العامة		البيانات العامة

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
3,494,741.28	البيانات العامة	2,489,744.08	البيانات العامة
17,473,706.38	البيانات العامة	12,448,720.38	البيانات العامة
698,948.26	البيانات العامة	497,948.82	البيانات العامة
3,494,741.28	البيانات العامة	2,489,744.08	البيانات العامة
32,333.00	البيانات العامة	29,583.00	البيانات العامة
4,134,485.25	البيانات العامة	0.00	البيانات العامة
29,328,955.44	البيانات العامة	17,955,740.35	البيانات العامة

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
50,351,145.66	البيانات العامة	38,810,424.59	البيانات العامة

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
50,351,145.66	البيانات العامة		البيانات العامة

البيانات العامة	البيانات العامة	البيانات العامة	البيانات العامة
Project Manager	البيانات العامة	Cost Control Engineer	البيانات العامة
Name:	البيانات العامة	Name:	البيانات العامة
Signature:	البيانات العامة	Signature:	البيانات العامة
Date:	البيانات العامة	Date:	البيانات العامة
Project Manager	البيانات العامة	Commercial Director	البيانات العامة
Name:	البيانات العامة	Name:	البيانات العامة
Signature:	البيانات العامة	Signature:	البيانات العامة
Date:	البيانات العامة	Date:	البيانات العامة






Samco-National Construction Company

Project: The Big Project

(Statement of Works Invoice" BD-CW-SAMCO-ACE-INV-002-R00" for the big Project)

item	Description	Unit	Approved/submitted Quantity	Executed Quantity	WBS %	Payable %	%Progress	% Com. Progress	Reference
BOQ items									
Excavation	Excavation in ordinary soil for depth as per soil investigation report including transporting the excavation materials to the public dumping areas and getting ride of any excavation disposals	m3	2010.32	2010.32	100%	100%	100.00%	100.00%	BD-CW-SAMCO-PCO-QS-SUR-001-R00
			400.63	400.63	100%		100.00%		BD-CW-SAMCO-PCO-QS-SUR-002-R00
			578.09	578.09	100%		100.00%		BD-CW-SAMCO-PCO-QS-SUR-004-R01
PC	03300 Plain Concrete (PC) Grade 200 kg/cm² of OPC and minimum cement content 250 kg/m³ Blinding layer 300mm thickness	m3	2267.67	2018.23	100%	100%	89.00%	89.00%	BD-CW-SAMCO-ACE-QS-STR-001-R00
RC	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3 (B1 Raft)	m3	2194.89	2194.89	10%	26.82%	100.00%	100%	BD-CW-SAMCO-ACE-QS-STR-003-R00
	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3 (B2 Raft)	m3	1535.33	1535.33	40%		100.00%		BD-CW-SAMCO-ACE-QS-STR-003-R00
	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3 (B3 Raft)	m3	1111.77	1111.77	93%		100.00%		BD-CW-SAMCO-ACE-QS-STR-003-R00
	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3 (B4 Raft)	m3	2122.09	2122.09	0%		100.00%		BD-CW-SAMCO-ACE-QS-STR-003-R00
	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3 (TANK Raft)	m3	991.94	198.39	20%	20%	100.00%	100.00%	BD-CW-SAMCO-ACE-QS-STR-006-R00
WaterProofing SBS Horizontal only	SBS Water proofing membrane of a minimum thickness 4.0mm including protection board for vertical surfaces and protection screed for horizontal surfaces and all needed precautions, accessories, and material as per manufacturing requirements.	m2	7434.75	6616.93	100%	100%	89.00%	89.00%	BD-CW-SAMCO-ACE-QS-STR-004-R00
Steel	Deformed high yield steel bars with Different nominal size Used in Raft, Rc Columns, Rc Slabs and all concrete Items	ton	146.8	146.8	100%	100%	100.00%	100%	SAMCO-PCO-MIR-STR-015-R00
			440.18	440.18	100%		100.00%		SAMCO-PCO-MIR-STR-050-R00
			11.975	11.975	100%		100.00%		SAMCO-PCO-MIR-STR-056-R01
			30.625	30.625	100%		100.00%		SAMCO-PCO-MIR-STR-057-R01
			69.425	69.425	100%		100.00%		SAMCO-PCO-MIR-STR-058-R01
Variation items									
Soil Replacement	By m3, Replacement Layer Supply and Installation of a 2:1 mix of crushed stone and clean sand to the specified thickness and levels as per the drawings and Engineer's directions. The material is to be applied in layers not exceeding 25 cm loose thickness, moisture-conditioned, and mechanically compacted to achieve the required compaction as per project specifications and geotechnical recommendations.	m3	4422.041	4422.041	100%	100%	86.040%	86.040%	BD-CW-SAMCO-PCO-QS-SUR-005-R00
			5871.648	5871.648					BD-CW-SAMCO-PCO-QS-SUR-006-R01
			1670.152	0					BD-CW-SAMCO-PCO-QS-SUR-007-R00
Geogride & Geocell	By m2, supplying and installing two layers of TX160 geogrid with a tensile strength of 40 kN/m and a 10 cm high geocell layer, as per the levels indicated in the construction drawings and soil recommendation report. The rate excludes earthworks or backfilling inside the geocell.	m2	7389.26	6502.32	100%	100%	87.997%	87.997%	BD-CW-SAMCO-ACE-QS-STR-002-R00
Technical Office Name: <i>[Signature]</i> Signature: Date: 									





ACE-PM
MOHARRAM BAKHOUM

PRIME
CONSULTING OFFICE



Over Time For Supervision Engineer

1	The Supervision Fees /day	No of Hours	No of days	Prev.	Current	Comulative Amount
		2000	129.332	16.1665	29,583.00	2,750.00
						32,333.00



ROYA



ACE-PM
MOHARRAM BAKHOUM




PRIME
CONSULTING OFFICE




NO.	Description	QTY	RATE	Price of Concrete in the Contract	Concrete in the Contract (Exclud	Weight of VAT according to BOQ Rates	DEDUCTED AMOUNT	
1	PC Concrete grade 200/ Cement Content 250	2,018.23	3625	7,316,083.75	2000	1754.39	495,705.61	6.78%
2	SOG Concrete grade 250/ Cement Content 300		10333.33	-	2250	1973.68	-	2.67%
3	RC Raft Concrete grade 350/ Cement Content 400	1,867.57	7210	13,465,158.79	2500	2192.98	573,375.86	4.26%
4	RC Retaining Walls Concrete grade 350/ Cement Content 400		9900	-	2500	2192.98	-	3.10%
	RC Tanks Concrete grade 350/ Cement Content 400	198.39	9400	1,864,847.20	2500	2192.98	60,908.60	3.27%
	RC Col. - Walls Below SOG Concrete grade 350/ Cement Content 400		9100	-	2500	2192.98	-	3.37%
	columns Concrete grade 300/ Cement Content 300		9470	-	2350	2061.40	-	3.05%
	slabs Concrete grade 300/ Cement Content 300		9580	-	2350	2061.40	-	3.01%
	beams Concrete grade 300/ Cement Content 300		9675	-	2350	2061.40	-	2.98%
	shear walls Concrete grade 300/ Cement Content 300		9465	-	2350	2061.40	-	3.05%
	stairs Concrete grade 300/ Cement Content 300		9360	-	2350	2061.40	-	3.08%
	High yield steel bars	699.01	40620	28,393,583.10	35000	30701.75	3,004,495.18	10.58%
	TOTAL			51,039,672.84			4,134,485.25	0.08

Signature



Item no.	Description of Works	Unit	Accepted Contract Amount			General Requirements							Remarks
			Qty.	Unit Rate	Total Amount	Quantities			progress %	Total Amount			
						Prev.	Current	Total		Prev.	Current	Total	
	DIVISION 2: SITE CONSTRUCTION												
	Site Clearance General Site clearing, grabbing and demolishing of obstacles with off-site disposal												
2	Excavation and Earthwork												
2.1	Excavation in ordinary soil for depth as per soil investigation report including transporting the excavation materials to the public dumping areas and getting ride of any excavation disposals	m3	0.00	180.00	-	2,989.04	0.00	2,989.04	100%	538,027.20	0.00	538,027.20	
2.2	Excavation in rock for depth as per soil investigation report including transporting the excavation materials to the public dumping areas and getting ride of any excavation disposals	m3	0.00	450.00	-	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2.3	Replacement Soil in accordance with the geotechnical report recommendations including all compaction and necessart tests	m3	12000.00	633.00	7,596,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2.5	Back filling above the foundation and below slab on grade with siliceous clean sand installed in successive lifts, 0.25m thick compacted to not less than 95% using modified Proctor test	m3	6800.00	460.00	3,128,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	DIVISION 3: CONCRETE												
	Structural Concrete Supply and install concrete, including Furnishing, installing materials, concrete materials, aggregate, water, mixing, additives, grading and trowelling, Fiber reinforcement, substrate preparation, protection, covering, cleaning, repairing of defective screed, and any other required items as per Drawings and Snarifications												
1	03300 Plain Concrete (PC) Grade 200 kg/cm² of OPC and minimum cement content 250 kg/m³ Blinding layer 300mm thickness		2230.00	3625.00	8,083,750.00	1,957.68	60.55	2,018.23	100%	7,096,601.24	219,482.51	7,316,083.75	
	03300 Reinforced concrete (RC) Grade 350 kg/cm2 of OPC and minimum cement content 400 kg/m³												
1	Raft Foundation	m3	6550.00	7210.00	47,225,500.00	0.00	1,867.57	1,867.57	100%	0.00	13,465,158.79	13,465,158.79	
2	Retaining Walls	m3	790.00	9900.00	7,821,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
3	Tanks	m3	800.00	9400.00	7,520,000.00	0.00	198.39	198.39	100%	0.00	1,864,847.20	1,864,847.20	
4	Columns & Walls below SOG	m3	100.00	9100.00	910,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	03300 Reinforced concrete (RC) Grade 300 kg/cm2 of OPC and minimum cement content 300 kg/m³												
1	Columns	m3	1560.00	9470.00	14,773,200.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2	slabs	m3	10500.00	9580.00	100,590,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
3	Beams	m3	215.00	9675.00	2,080,125.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
4	Shear walls	m3	1590.00	9465.00	15,049,350.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
5	Stairs	m3	260.00	9360.00	2,433,600.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	03300 Reinforced concrete (RC) Grade 250 kg/cm2 of OPC and minimum cement content 300 kg / m³												
1	Slab on grade 150mm thickness	m2	6370.00	1550.00	9,873,500.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	Deformed high yield steel bars with Different nominal size Used in Raft, Rc Columns, Rc Slabs and all concrete Items	ton	3300.00	40620.00	134,046,000.00	586.98	112.03	699.01	100%	23,843,127.60	4,550,455.50	28,393,583.10	
	Fence												
1	Precast concrete fence With Height 2.5 m	l.m	0.00	6500.00	-	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2	Corrugated sheet fence	l.m	0.00	3500.00	-	0.00	0.00	0.00	0%	0.00	0.00	0.00	
	DIVISION 7: THERMAL AND MOISTURE PROTECTION												
	07130 SHEET WATERPROOFING												
	Supply and install sheet waterproofing including furnishing materials, protection mat, sealants and sheet flashing, preparation of substrates, cutting, rounding, intersections, prime coat, and side overlapping to vertical surfaces, reglets and bending free edge in grooving, testing, replacing of damaged membrane, protection, covering and cleaning, and any other required items as per Drawings and Specifications												
1	SBS water prooting memorane of a minimum thickness 4.0mm including protection board for vertical surfaces and protection screed for horizontal surfaces and all needed precautions, accessories, and material as per manufacturing requirements.	m2	9500.00	450.00	4,275,000.00	6,616.93	0.00	6,616.93	100%	2,977,618.50	0.00	2,977,618.50	
	07140 COLD FLUID-APPLIED WATERPROOFING												
	Supply and install Cold applied waterproofing including furnishing materials, protection mat, sealants and sheet flashing, preparation of substrates, cutting, rounding, intersections, prime coat, and side overlapping to vertical surfaces, reglets and bending free edoe.in aroovino. testino. reolacino of damaaed membrane.												
1	Cold applied damp-proofing for top side of raft and underground concrete surfaces in contact with soil/backfill,	m2	7,600.00	90.00	684,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
2	Cold applied Crystalline Waterproofing for water tanks	m2	1,900.00	630.00	1,197,000.00	0.00	0.00	0.00	0%	0.00	0.00	0.00	
Total Amount of Work					367,286,025.00					34,455,374.54	20,099,944.00	54,555,318.54	
 Technical Officer Signature: _____													



ROYA



ACE-PM
MOHARRAM BAKHOUM

PRIME
CONSULTING OFFICE



Item no.	Description of Works	Unit	Accepted Contract Amount			General Requirements							Remarks	
			Qty.	Unit Rate	Total Amount	Quantities			progress %	Total Amount				
						Prev.	Current	Total		Prev.	Current	Total		
	Variation Order : (BD-CW-SAMCO-ACE-VOR-001-R00)													
	Earthwork													
1	By m3, Replacement Layer Supply and Installation of a 2:1 mix of crushed stone and clean sand to the specified thickness and levels as per the drawings and Engineer's directions. The material is to be applied in layers not exceeding 25 cm loose thickness, moisture-conditioned, and mechanically compacted to achieve the required compaction as per project specifications and geotechnical recommendations.	m3	12000.00	792.28	9,507,360.00	10,293.689	0.000	10,293.689	100%	8,155,483.76	0.00	8,155,483.76		
2	By m2, supplying and installing two layers of TX160 geogrid with a tensile strength of 40 kN/m, and a 10 cm high geocell layer, as per the levels indicated in the construction drawings and soil recommendation report. The rate excludes earthworks or backfilling inside the geocell.	m2	7850.00	1104.84	8,672,994.00	6,502.320	0.00	6,502.320	100%	7,184,023.23	0.00	7,184,023.23		
Total Amount of Work					18,180,354.00					15,339,506.99	0.00	15,339,506.99		


Technical Office

SAMCO

The Big P

Name :
Signature

Date:



Technical Office
Name :
Signature:
Date:


Signature



The Big

DOCUMENT SUBMITTAL (DS)

Project: The Big Business District
 Owner: ROYA Developments
 Project Manager: ACE
 Supervision Consultant: PRIME CONSULTING
 Contractor: SAMCO National Construction
 TO: PCO
 CC: --



DS/Submittal No.	Rev.
BD-CW-SAMCO-PCO-DS-STR-085-R00	0
Date: 21/01/2026	
Submitted For	
Approval	1
Information	2
Action (2)	
Approved	A
Approved as Noted	B
Revise and Resubmit	C
Rejected	D

WE TRANSMIT HERewith / UNDER SEPARATE COVER, THE DRAWINGS, CALCULATION, ETC. LISTED BELOW DATE 21/1/2026

ITEM NO.	DRW., SPEC OR BOQ. REF	QTY	DESCRIPTION	TYPE +	SUBMITTAL CODE *	ACTION CODE **
1	Sheet	1	Progress of Invoice (No.03) for the Big Business District Project			
Attachments:- (1) A4 (3) A3 Sheets * (2) COPIES						

CONTRACTOR :

RECEIVED BY :

COPIES:



DATE :

DATE :

Consultant to enter ACTION CODE and REMARKS

Supervision Consultant Remarks :

For the executed works follow the shown ^{Comments} instructions in the attached drawings.

Eng. Iman Mounir

Supervision Consultant:

DATE : 21.1.2026

Corrections or comments made relative to submittals during this review does not relieve the contractor from compliance with the requirements of the drawings and specifications. This check is only for review of general conformance with the design concept of the project and general compliance with the information given in the contract documents. The contractor is responsible for confirming and correlating all quantities and dimensions, selecting fabrication process and techniques of construction, coordinating his work with that of other trades, and performing his work in a safe and satisfactory manner.

Project Manager Remarks (If Required):



Project Manager:

DATE :

Received by Contractor:

DATE :

COPIES:

+ TYPE: SD Shop Drawings
 SM Sample
 GT Guarantee
 MD Manufacturer's Data
 CT Certificate
 OT Others

RECEIVED

SAMCO

THE BIG BUSINESS DISTRICT

DATE: 22/1/2026

SUBMITTAL CODE:

1 Submitted for Approval
 2 Submitted for Information

** ACTION CODE:

A: Approved
 B: Approved as Noted
 C: Revise and Resubmit
 D: Rejected

Structure

Architecture

Surveying

Electrical

Mechanical

Landscape

Infra & Roads

Other

ROYA


ACE-PM
 MOHARRAM BAKHOUM

PRIME
 CONSULTING OFFICE


Samco-National Construction Company

Project: The Big Project

(Statement of Works Invoice" BD-CW-SAMCO-ACE-INV-002-R00" for the big Project)

Item	Description	Unit	Approved/submitted Quantity	Executed Quantity	Total Executed Quantity	%Progress	Reference
BOQ items							
Excavation	Excavation in ordinary soil for depth as per soil investigation report including transporting the excavation materials to the public dumping areas and getting ride of any excavation disposals	m3	2010.32	2010.32	2989.04	100.00%	BD-CW-SAMCO-PCO-QS-SUR-001-R00
			400.63	400.63			BD-CW-SAMCO-PCO-QS-SUR-002-R00
			578.09	578.09			BD-CW-SAMCO-PCO-QS-SUR-004-R00
PC	03300 Plain Concrete (PC) Grade 200 kg/cm² of OPC and minimum cement content 250 kg/m³ Blinding layer 300mm thickness	m3	2267.67	2018.23	2018.23	89.00%	BD-CW-SAMCO-ACE-QS-STR-001-R00
RC	(03300) Reinforced concrete (RC) Grade 350 kg /cm² of OF OPC and minimum cement content 400 kg/m³ (B1)	m3	2194.89	0.00	2647.10	38.01%	BD-CW-SAMCO-ACE-QS-STR-003-R00
	(03300) Reinforced concrete (RC) Grade 350 kg /cm² of OF OPC and minimum cement content 400 kg/m³ (B2)	m3	1535.33	1535.33			BD-CW-SAMCO-ACE-QS-STR-003-R00
	(03300) Reinforced concrete (RC) Grade 350 kg /cm² of OF OPC and minimum cement content 400 kg/m³ (B3)	m3	1111.77	1111.77			BD-CW-SAMCO-ACE-QS-STR-003-R00
	(03300) Reinforced concrete (RC) Grade 350 kg /cm² of OF OPC and minimum cement content 400 kg/m³ (B4)	m3	2122.09	0.00			BD-CW-SAMCO-ACE-QS-STR-003-R00
	(03300) Reinforced concrete (RC) Grade 350 kg /cm² of OF OPC and minimum cement content 400 kg/m³ (TANK)	m3	991.94	198.39	198.39	20.00%	BD-CW-SAMCO-ACE-QS-STR-006-R00
WaterProofing SBS Horizontal only	SBS Water proofing membrane of a minimum thickness 4.0mm including protection board for vertical surfaces and protection screed for horizontal surfaces and all needed precautions, accessories, and material as per manufacturing requirements.	m2	7434.75	6616.93	6616.93	89.00%	BD-CW-SAMCO-ACE-QS-STR-004-R00
Steel	Deformed high yield steel bars with Different nominal size Used in Raft, Rc Columns, Rc Slabs and all concrete Items	ton	146.8	146.8	699.005	100.00%	SAMCO-PCO-MIR-STR-015-R00
			440.18	440.18			SAMCO-PCO-MIR-STR-050-R00
			11.975	11.975			SAMCO-PCO-MIR-STR-056-R01
			30.625	30.625			SAMCO-PCO-MIR-STR-057-R01
			69.425	69.425			SAMCO-PCO-MIR-STR-058-R01
Variation items							
Soil Replacement	By m3, Replacement Layer Supply and Installation of a 2:1 mix of crushed stone and clean sand to the specified thickness and levels as per the drawings and Engineer's directions. The material is to be applied in layers not exceeding 25 cm loose thickness, moisture-conditioned, and mechanically compacted to achieve the required compaction as per project specifications and geotechnical recommendations.	m3	4422.041	4422.041	10293.69	86.040%	BD-CW-SAMCO-PCO-QS-SUR-005-R00
			5871.648	5871.648			BD-CW-SAMCO-PCO-QS-SUR-006-R01
			1670.152	0			BD-CW-SAMCO-PCO-QS-SUR-007-R00
Geogride & Geocell	By m2, supplying and installing two layers of TX160 geogrid with a tensile strength of 40 kN/m, and a 10 cm high geocell layer, as per the levels indicated in the construction drawings and soil recommendation report. The rate excludes earthworks or backfilling to fill the geocell.	m2	7389.26	6502.32	6502.32	87.997%	BD-CW-SAMCO-ACE-QS-STR-002-R00

Technician Office

Name :

Signature :

Date :



ACE-PM
 MOHARRAM BAKHOUM
 THE BIG



Samco-National Construction Company
Project: The Big Project
(progress of the First Invoice for the big Project)




Item	Description	Unit	QS NO	Progress Percentage	Notes
B.O-Q ITEMS					
Excavation	Excavation in ordinary soil for depth as per soil investigation report including transporting the excavation materials to the public dumping areas and getting ride of any excavation disposals	m3	QS-SUR-001	100%	The quantity is approved and executed at 100% as per the As-Built implementation
			QS-SUR-002	100%	
			QS-SUR-004-R01	100%	
PC	03300 Plain Concrete (PC) Grade 200 kg/cm² of OPC and minimum cement content 250 kg/m³ Blinding layer 300mm thickness	m3	QS-STR-01	89%	According to the attached drawings
RC	(03300) Reinforced concrete (RC) Grade 350 kg /cm2 of OF OPC and minimum cement content 400 kg/m3	m3	QS-STR-03&06	87%	According to the attached drawings (Form work)
				42%	According to the attached drawings (Casting)
Membrane SBS	SBS Water proofing membrane of a minimum thickness 4.0mm including protection board for vertical surfaces and protection screed for horizontal surfaces and all needed precautions, accessories, and material as per manufacturing requirements.	m2	QS-STR-04	89%	According to the attached drawings
Steel	Deformed high yield steel bars with Different nominal size Used in Raft, Rc Columns, Rc Slabs and all concrete items	ton	QS-STR-14	46%	According to the attached drawings (reinforcement)
			MIR-STR-015&MIR-STR-050&STR-056rev01&STR-057rev01&STR-058rev01	100%	According to the approved MIR
Variation Orders ITMES					
Soil Replacement	By m3, Replacement Layer Supply and Installation of a 2:1 mix of crushed stone and clean sand to the specified thickness and levels as per the drawings and Engineer's directions. The material is to be applied in layers not exceeding 25 cm loose thickness, moisture-conditioned, and mechanically compacted to achieve the required compaction as per project specifications and geotechnical recommendations.	m3	QS-SUR-005	100%	The quantity is approved and executed 100% as per the As-Built implementation
			QS-SUR-006-rev01	100%	The quantity is approved and executed 100% as per the As-Built implementation
Geogride & geocell	By m2, supplying and installing two layers of TX160 geogrid with a tensile strength of 40 kN/m, and a 10 cm high geocell layer, as per the levels indicated in the construction drawings and soil recommendation report. The rate excludes earthworks or backfilling inside the geocell.	m2	QS-STR-02	88%	According to the attached drawings

Consultant

MAIN CONTRACTOR



TX-160 & GEOCELL-10CM

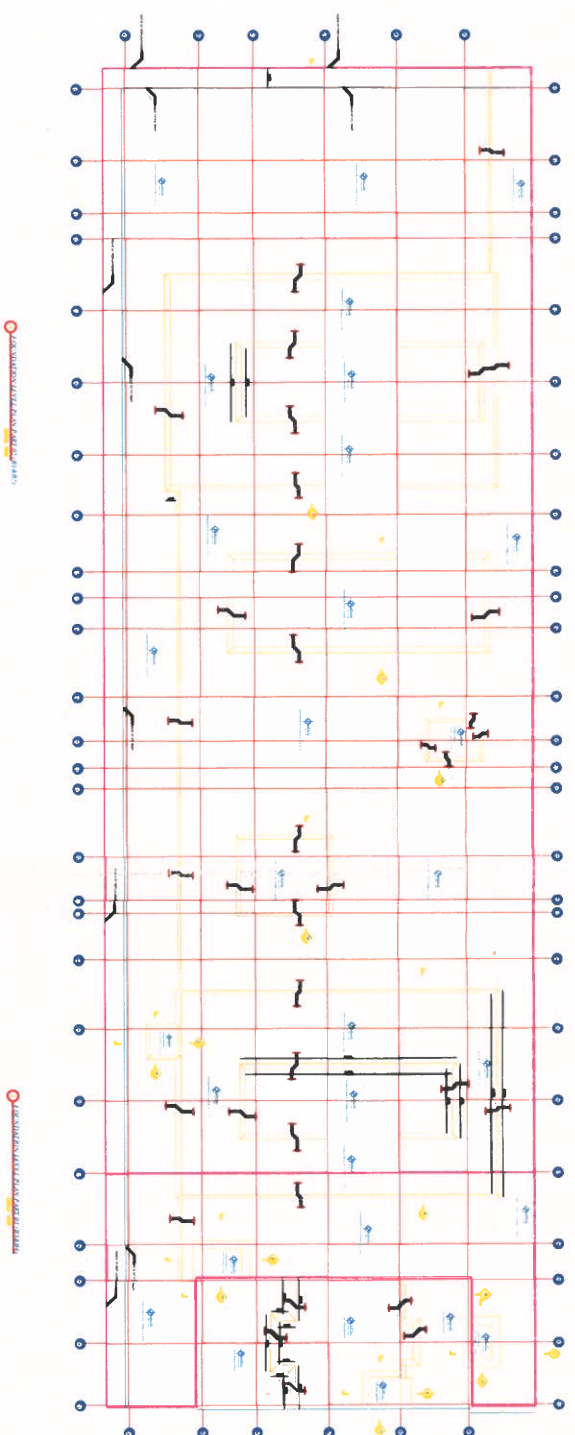


%100

%88



P.C

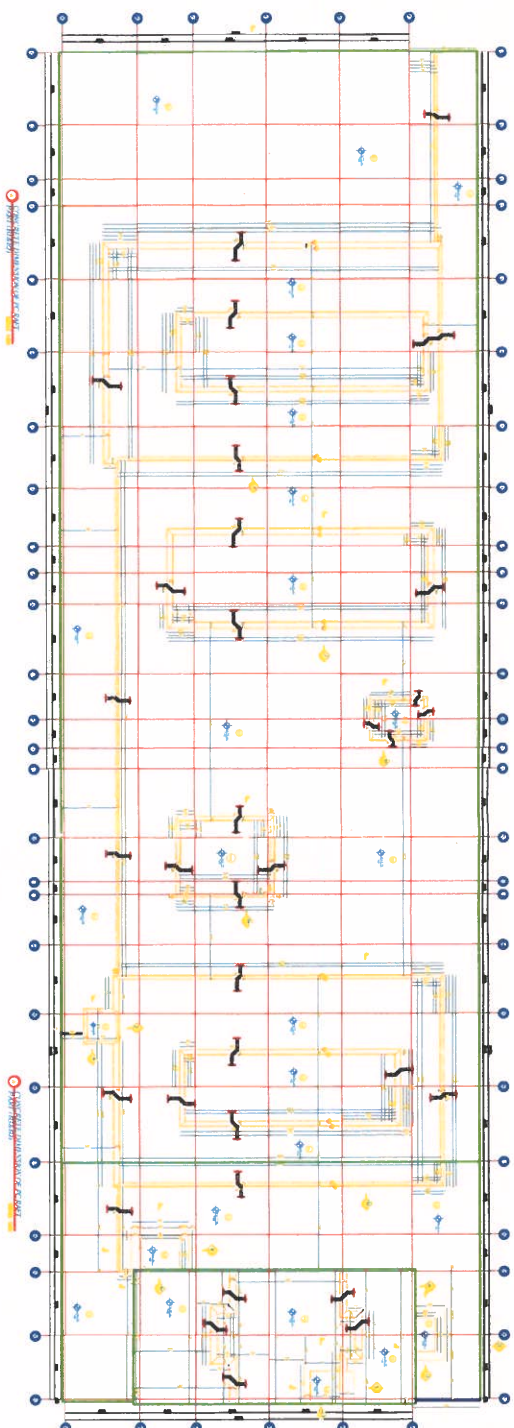

%100

Total P.C
Works




%89

Work
completed



Membrane Insulation

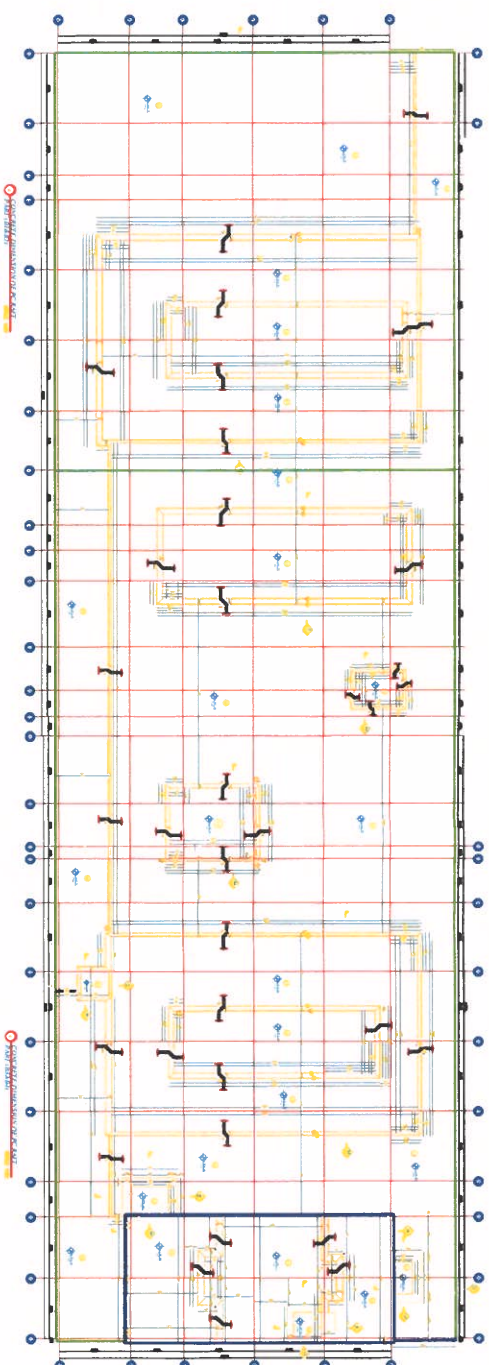


%100


total
membrane
sbs works

%89


Work
completed

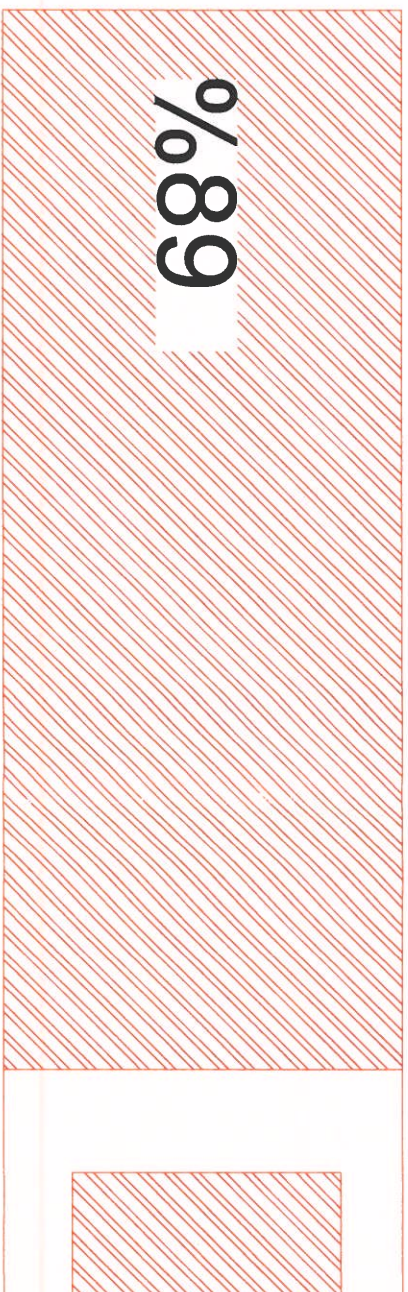


Form work raft

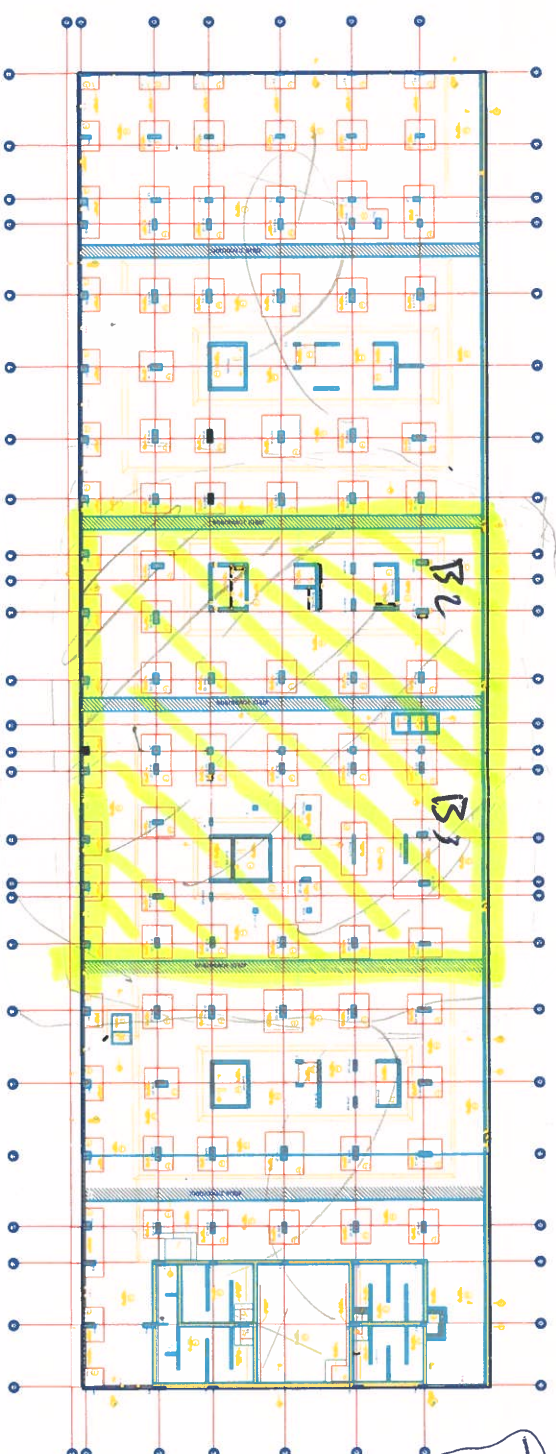

The inspected and approved formwork is only for Buildings (B2, B3) Eng/amer mason

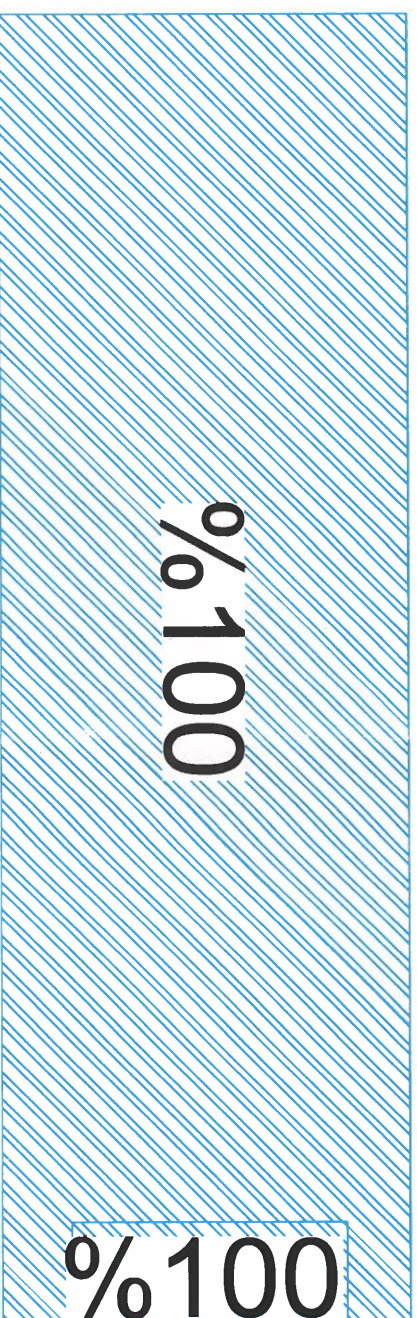


total foam works

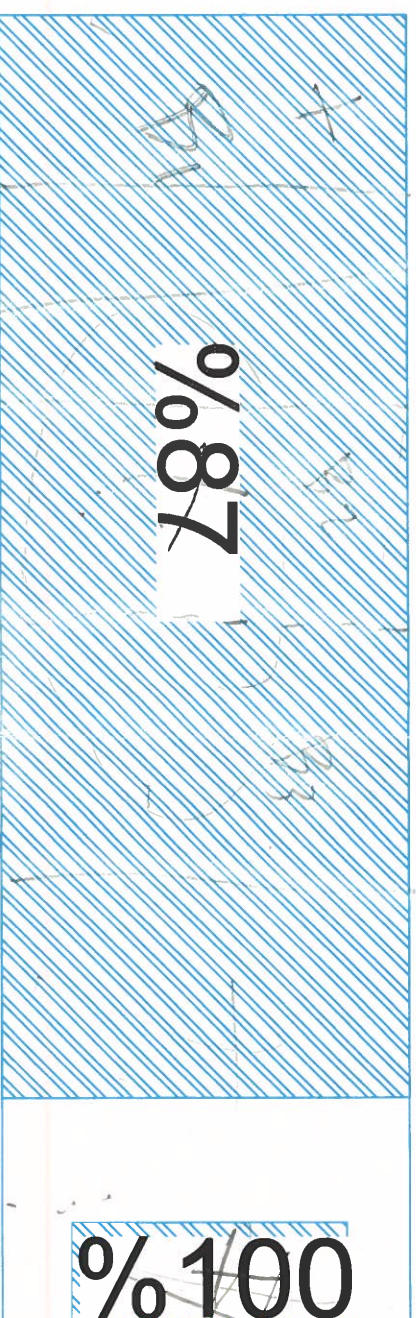

Work completed



reinforcement raft

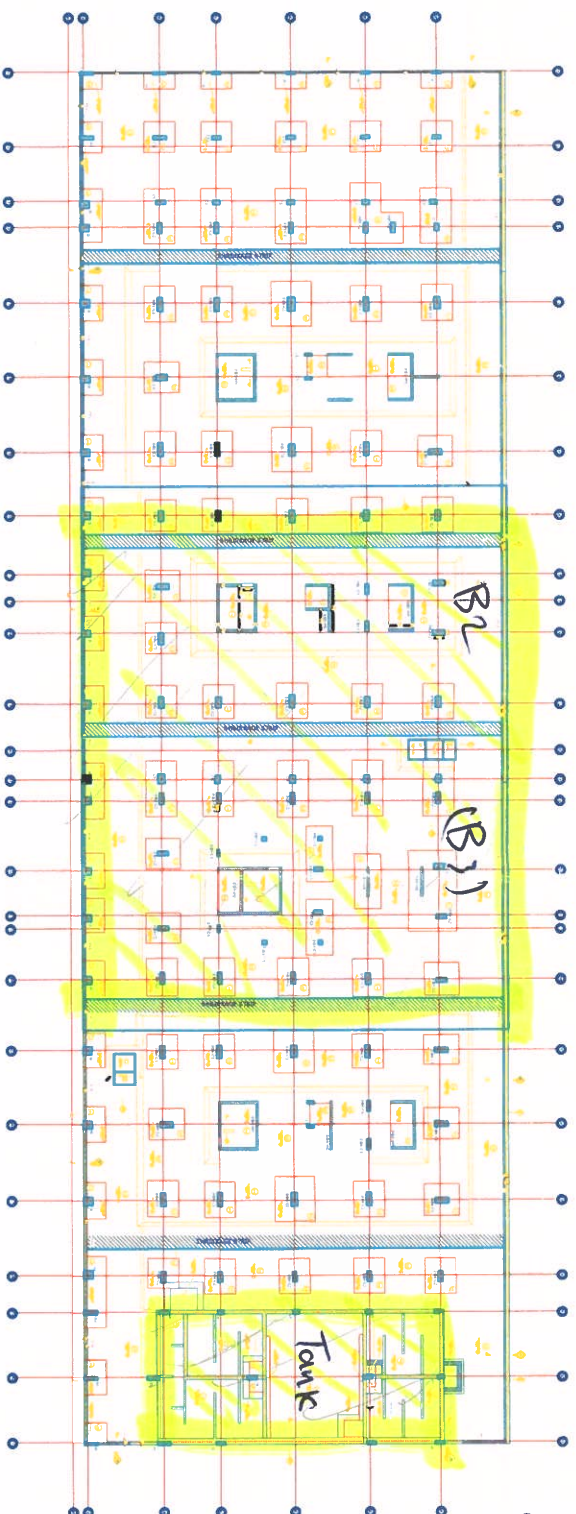

Reinforcement works for (B2, B3, Tank) RAFT is only the inspected and approved. Every lower mason.



%100


total
reinforcement
raft

%46

Work
completed



casting raft

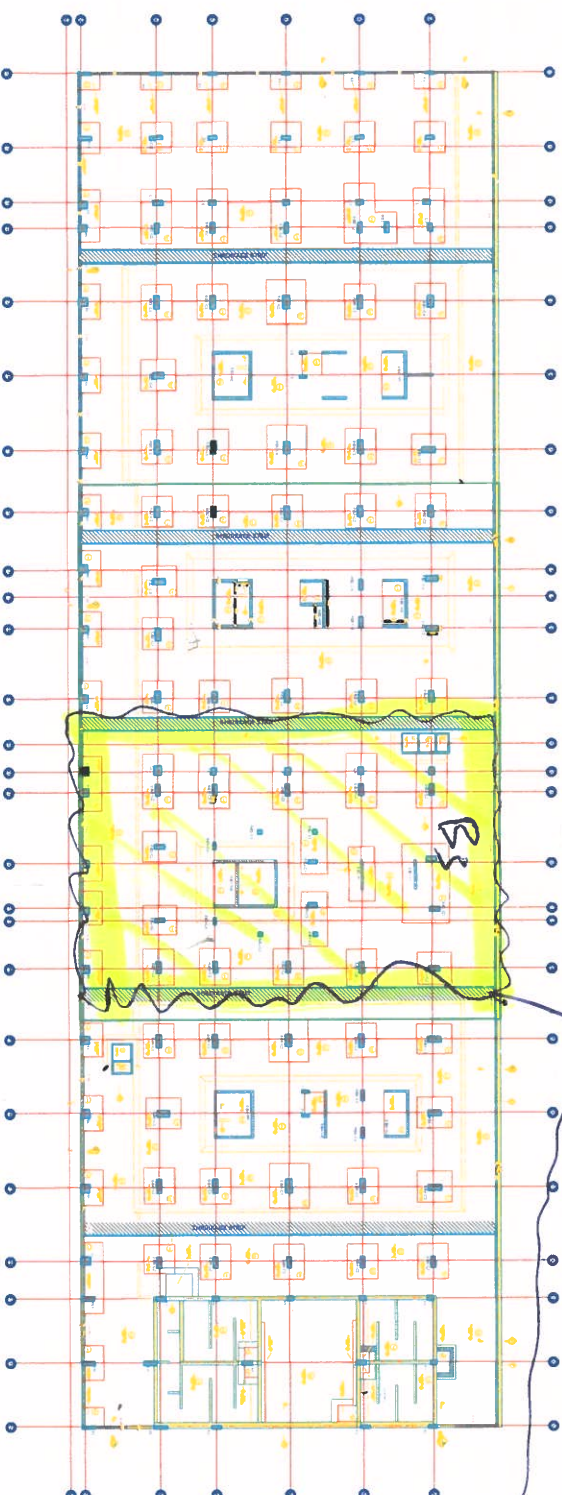

The Poured Building 15 (B3) only
Eng lower mura co.

%100

%100

total
casting

%42

Work
completed

