



Employee Free Issue Material Delay & Fragnet Insertion Methodology

Batch 1 & Batch 2 | Time Impact Analysis / Extension of Time

Project: The-BIG PH01

Analysis Cutoff: 05-May-2026

Consultant Submission | EOT: 117
Calendar Days

117 Days

Net EOT impact

-117 Days

Float movement

06-Sep-27

Post-fragnet finish

-149 TF

After fragnet

12-May-27

Pre-fragnet finish

Schedule Result

The steel supply delay fragnet was inserted in the 26-Nov-2025 update and recalculated using a 7-day calendar for Employer delay activities.

Calculated Impact

Project finish moved from 12-May-2027 to 06-Sep-2027. Total Float moved from -32 days to -149 days.


Event 01 EOT impact: 117 calendar days.

Date / Window	Cause / Event	Effect on Works	P6 Treatment
27-Oct-25	Batch 1 partial steel received	Partial release only; balance still required	Reference milestone
03-Nov-25 → 28-Dec-25	Batch 1 balance unavailable	Selected footing / WT RFT restrained	EOT-STL-B1-FM gate
27-Nov-25 → 15-Feb-26	Batch 2 first partial delayed	Part 1 RFT released after steel gate	EOT-STL-B2-MS gate
27-Nov-25 → 05-May-26	Batch 2 steel outstanding at cutoff	Part 2 RFT remains constrained	EOT-STL-B2-CUT gate


Cause & Effect Register

- Cause**Employer steel availability not achieved on planned dates.
- Effect**Selected RFT activities were held by the relevant steel gate.
- Control**Normal construction logic retained; steel gate added as FS predecessor.
- Result**Project finish moved by 117 calendar days after recalculation.

Effect Chain




Conclusion: the steel supply restraint was introduced as an activity-specific FS gate. The measured impact is based on Primavera finish-date movement, not arithmetic addition of steel delay durations.

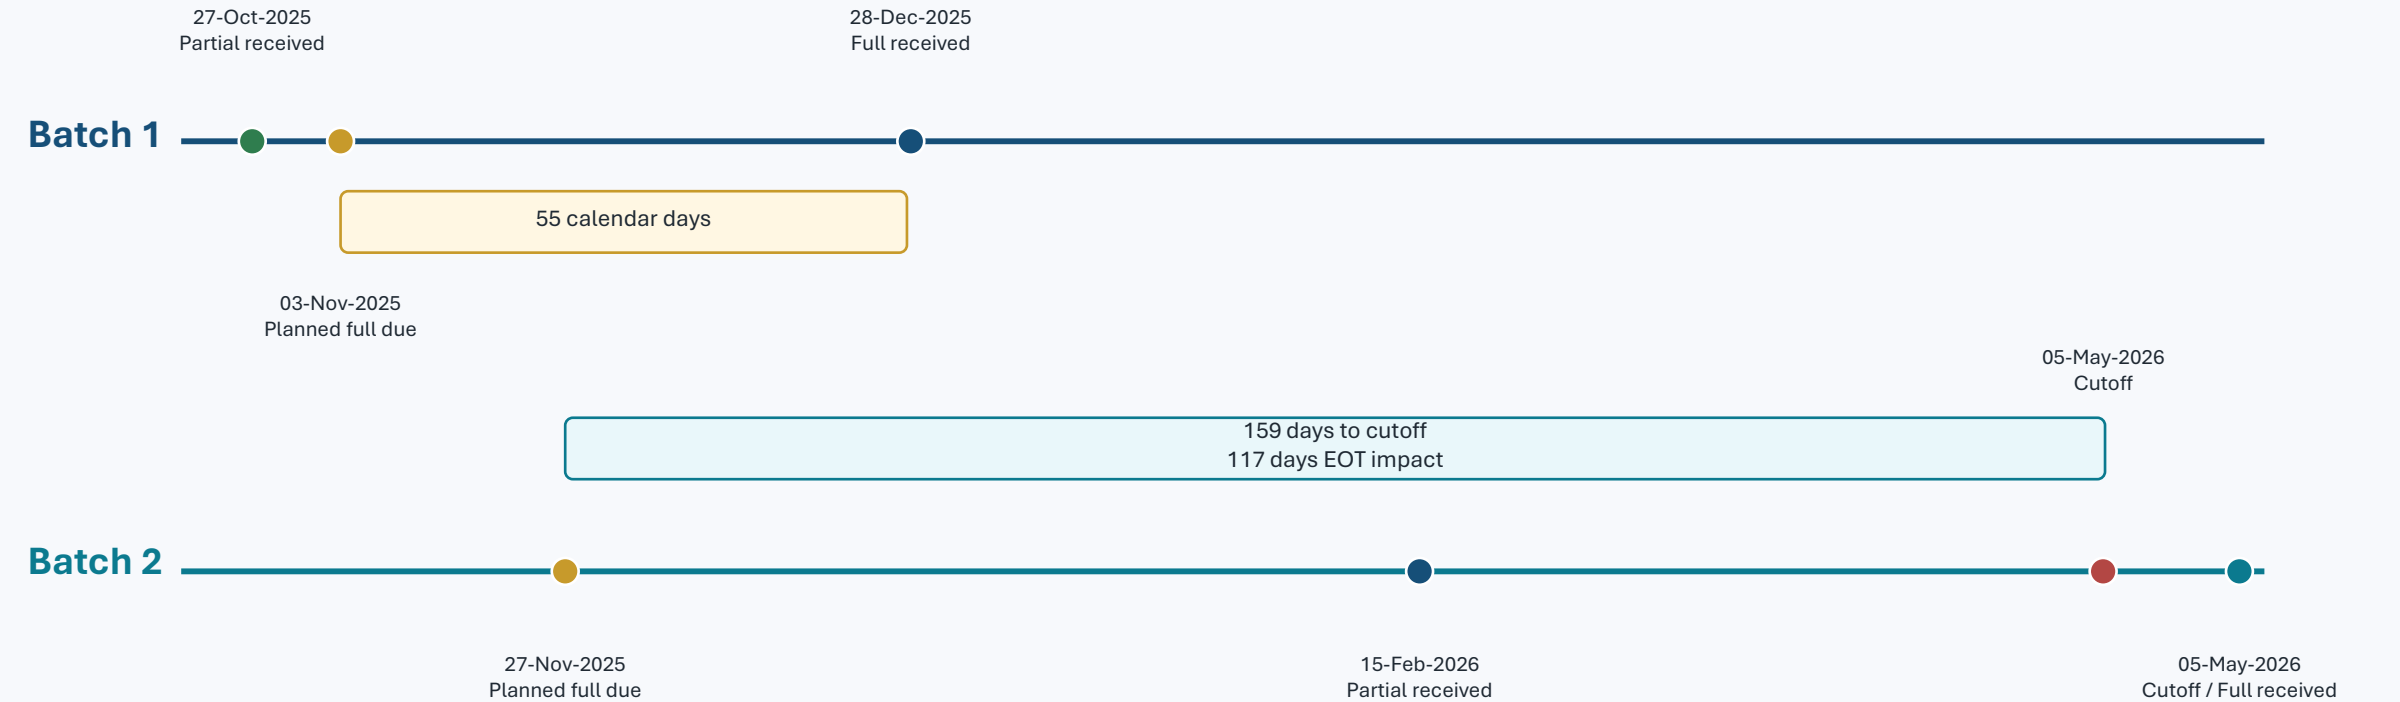

Data date: 26-Nov-2025. EOT measured by finish movement: 12-May-2027 to 06-Sep-2027.

Item	Date / Value	Treatment
Planned full supply	03-Nov-2025	Start milestone
Partial delivery	27-Oct-2025	Reference only
Full availability	28-Dec-2025	Finish milestone
Delay activity	55 calendar days	Task Dependent / 7-Day
Data Date	30-Oct-2025	Accepted update before event



Affected RFT Case	Normal Pred.	Steel Pred.	Rel.
Missing balance affects RFT	Shuttering-XXX	EOT-STL-B1-FM	FS + FS
Partial steel sufficient	Shuttering-XXX	No fragnet link	FS only

Construction Logic Linkage



Applied control: affected RFT activities retain their formwork/engineering logic and receive EOT-STL-B1-FM as an additional FS predecessor only where the missing Batch 1 balance restrained the work.


PRIMAVERA VIEW

Activity ID	Activity Name	Total Float	Original Duration	BL Project Start	BL Project Finish	Start	Finish
[-] ROYA-BIG PROJECT PHASE01 (B1-4)		0	589	11-Sep-25	22-Apr-27	11-Sep-25 A	22-Apr-27
[-] Event01-Batch01-Part02-Steel Delay		19	76	03-Nov-25	17-Jan-26	03-Nov-25	17-Jan-26
[-] Steel Supply Fragnet		-8	55	03-Nov-25	27-Dec-25	03-Nov-25	27-Dec-25
[-] EOT-STL-B1-SM	Batch 1 Planned Full Supply Due	-8	0	03-Nov-25		03-Nov-25*	
[-] EOT-STL-B1-DLY-01	Employer Delay to Batch 1 Balance	-8	55	03-Nov-25	27-Dec-25	03-Nov-25	27-Dec-25
[-] EOT-STL-B1-FM	Batch 1 Full Steel Available	-8	0		27-Dec-25		27-Dec-25
[-] Affected-Activities-linked-Gate		16	17	28-Dec-25	17-Jan-26	28-Dec-25	17-Jan-26
[-] CON-B04-WT-1220	RFT for RC Raft (B04) (Water Tank)	16	5	28-Dec-25	01-Jan-26	28-Dec-25	01-Jan-26
[-] CON-B03-FOOT-1130	RFT for RC Raft & Footings (B03) (footing)	7	10	28-Dec-25	08-Jan-26	28-Dec-25	08-Jan-26
[-] CON-B02-FOOT-1130	RFT for RC Raft & Footings (B02) (footing)	-7	10	28-Dec-25	08-Jan-26	28-Dec-25	08-Jan-26
[-] CON-B03-FOOT-1140	RFT for Columns & Walls Below SOG (B03) (footing)	8	5	01-Jan-26	06-Jan-26	01-Jan-26	06-Jan-26
[-] CON-B04-WT-1230	RFT for Walls (B04) (Water Tank)	16	8	08-Jan-26	17-Jan-26	08-Jan-26	17-Jan-26

Simulation of the Primavera P6 implementation for Batch 1 steel delay fragnet, including Part 2 full-delivery / cutoff date, and the affected-activities linked gate.


Item	Date / Value	Treatment
Planned full supply	27-Nov-2025	Start milestone
First partial delivery	15-Feb-2026	Partial gate
Cutoff date	05-May-2026	Cutoff gate
Full receipt	05-May-2026	Post-cutoff confirmation
Delay to cutoff	159/160 cal. days	7-Day P6 branch

Batch 2 Steel Fragnet

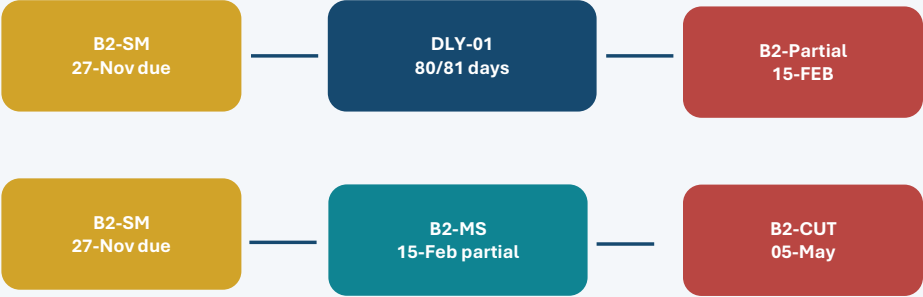


Activity Assignment Logic

Activities released by first partial delivery



Activities still affected at cutoff



PRIMAVERA VIEW

Event01-Batch02 Steel Delay		-109	225	27-Nov-25	09-Jul-26	27-Nov-25	09-Jul-26
Event01-Batch02-Part01-Steel Delay		-122	193	27-Nov-25	07-Jun-26	27-Nov-25	07-Jun-26
Steel Supply Fragnet		-33	81	27-Nov-25	15-Feb-26	27-Nov-25	15-Feb-26
■ EOT-STL-B2-SM	Batch02 Planned Full Supply Due	-33	0	27-Nov-25		27-Nov-25*	
■ EOT-STL-B2-DLY-01	Employer Delay to Batch02-Part01 Partial Delivery	-33	81	27-Nov-25	15-Feb-26	27-Nov-25	15-Feb-26
■ EOT-STL-B2-FM	Batch02-Part01 Partial Steel Partial Delivery	-33	0		15-Feb-26		15-Feb-26
Affected-Activities-linked-Gate		-95	87	16-Feb-26	07-Jun-26	16-Feb-26	07-Jun-26
■ F-CON-B04-FOOT-1050	RFT for RC Raft & Footings (B04) (footing)	-27	8	16-Feb-26	24-Feb-26	16-Feb-26	24-Feb-26
■ F-CON-B04-FOOT-1070	RFT for Columns & Walls Below SOG (B04) (footing)	-21	5	16-Feb-26	21-Feb-26	16-Feb-26	21-Feb-26
■ F-CON-B03-BAS02-1010	RFT for Walls, Col. & Cores (B03) (Bas 02)	-95	12	20-May-26	07-Jun-26	20-May-26	07-Jun-26
Event01-Batch02-Part02-Steel Delay		-109	225	27-Nov-25	09-Jul-26	27-Nov-25	09-Jul-26
Steel Supply Fragnet		-154	160	27-Nov-25	05-May-26	27-Nov-25	05-May-26
■ FR-CON-STL-B2-SM	Batch02 Planned Full Supply Due	-154	0	27-Nov-25		27-Nov-25*	
■ FR-CON-STL-B2-DLY-02	Employer Delay to Batch02-Part01 Complete Delivery	-154	160	27-Nov-25	05-May-26	27-Nov-25	05-May-26
■ FR-CON-STL-B2-FM	Batch02-Part02 Steel Complete Delivery	-154	0		05-May-26		05-May-26
Affected-Activities-linked-Gate		-88	51	06-May-26	09-Jul-26	06-May-26	09-Jul-26
■ F-CON-B01-FOOT-1050	RFT for RC Raft & Footings (B01) (footing)	-125	14	06-May-26	21-May-26	06-May-26	21-May-26
■ F-CON-B02-BAS02-1010	RFT for Walls, Col. & Cores (B02) (Bas 02)	-97	12	06-May-26	19-May-26	06-May-26	19-May-26
■ F-CON-B04-BAS02-1010	RFT for Walls, Col. & Cores (B04) (Bas 02)	-76	10	06-May-26	17-May-26	06-May-26	17-May-26
■ F-CON-B04-WT-1160	RFT for Top Slab (B04) (Water Tank)	-67	6	06-May-26	12-May-26	06-May-26	12-May-26
■ F-CON-B01-BAS02-1010	RFT for Walls, Col. & Cores (B01) (Bas 02)	-124	15	01-Jun-26	17-Jun-26	01-Jun-26	17-Jun-26
■ F-CON-B02-BAS02-1060	RFT for Slabs & Beams (B02) (Bas 02)	-94	10	02-Jun-26	13-Jun-26	02-Jun-26	13-Jun-26
■ F-CON-B04-BAS02-1060	RFT for Slabs & Beams (B04) (Bas 02)	-76	10	03-Jun-26	14-Jun-26	03-Jun-26	14-Jun-26
■ F-CON-B04-BAS02-1080	RFT for Stairs (B04) (Bas 02)	-63	5	04-Jun-26	09-Jun-26	04-Jun-26	09-Jun-26
■ F-CON-B02-BAS02-1070	RFT for Stairs (B02) (Bas 02)	-97	6	04-Jun-26	10-Jun-26	04-Jun-26	10-Jun-26
■ F-CON-B04-BAS02-1090	RFT for Ramps (B04) (Bas 02)	-64	5	06-Jun-26	10-Jun-26	06-Jun-26	10-Jun-26
■ F-CON-B03-BAS02-1060	RFT for Slabs & Beams (B03) (Bas 02)	-95	10	16-Jun-26	27-Jun-26	16-Jun-26	27-Jun-26
■ F-CON-B03-BAS02-1070	RFT for Stairs (B03) (Bas 02)	-87	6	18-Jun-26	24-Jun-26	18-Jun-26	24-Jun-26
■ F-CON-B01-BAS02-1070	RFT for Slabs & Beams (B01) (Bas 02)	-124	10	28-Jun-26	09-Jul-26	28-Jun-26	09-Jul-26
■ F-CON-B01-BAS02-1080	RFT for Stairs (B01) (Bas 02)	-121	6	29-Jun-26	06-Jul-26	29-Jun-26	06-Jul-26
■ F-CON-B01-BAS02-1090	RFT for Ramps (B01) (Bas 02)	-123	8	29-Jun-26	08-Jul-26	29-Jun-26	08-Jul-26

Simulation of the Primavera P6 implementation for Batch 2 steel delay fragnet, including Part 1 partial-delivery logic, Part 2 cutoff logic, and the affected-activities linked gate.

Primavera Result

06-Sep-2027 – 12-May-2027 = 117 calendar days

Schedule Movement

Project finish moved from 12-May-2027 to 06-Sep-2027 after insertion and recalculation of the steel supply fragnet.

EOT Position

Claimed Event 01 EOT impact: 117 calendar days.



Measure	Before Fragnet	After Fragnet	Net Movement
Total Float	-32 days	-149 days	-117 days
Project Finish	12-May-2027	06-Sep-2027	117 days
Event 01 EOT	Steel fragnet	7-day calendar	117 days
Net Movement	Steel fragnet	7-day calendar	117 days

Submission Conclusion

The calculated Event 01 steel supply delay impact is 117 calendar days, based on Primavera finish-date movement from 12-May-2027 to 06-Sep-2027 and Total Float movement from -32 to -149 days.
