

Earned Value Management

?

BAC

EGP

2,100,000,000

Budget at Completion

?

AC

EGP

1,155,177,564

Actual Cost

?

EV

EGP

1,166,846,024

Earned Value

?

PV

EGP

1,112,493,976

Planned Value

?

Schedule Variance

EGP 54,352,048

Ahead of Schedule

?

Cost Variance

EGP 11,668,460

Under Budget

?

EAC

EGP

2,088,331,540

Estimate at Completion

?

TCPI

1.000

To Complete Performance Index

Critical Alerts

View All

!

Steel Supply Delay

Delay in steel shipment affecting structure building progress

High

!

IFC Clash Detected

4 clashes found in current coordination records

High

?

RFIs Pending

5 RFIs are pending response from consultants

Medium

?

Contract Exposure

Exposure amount exceeds threshold for active contracts

Medium

Performance Overview

Overall Progress

33.0%

Actual Complete

Planned Progress

31.0%

Baseline Plan

?

Contract Value

EGP

2,100,000,000

Total Contract Value

?

Actual Cost

EGP



1,155,177,564

55.0% of BAC

Remaining Duration

55.7%

364 Days Left

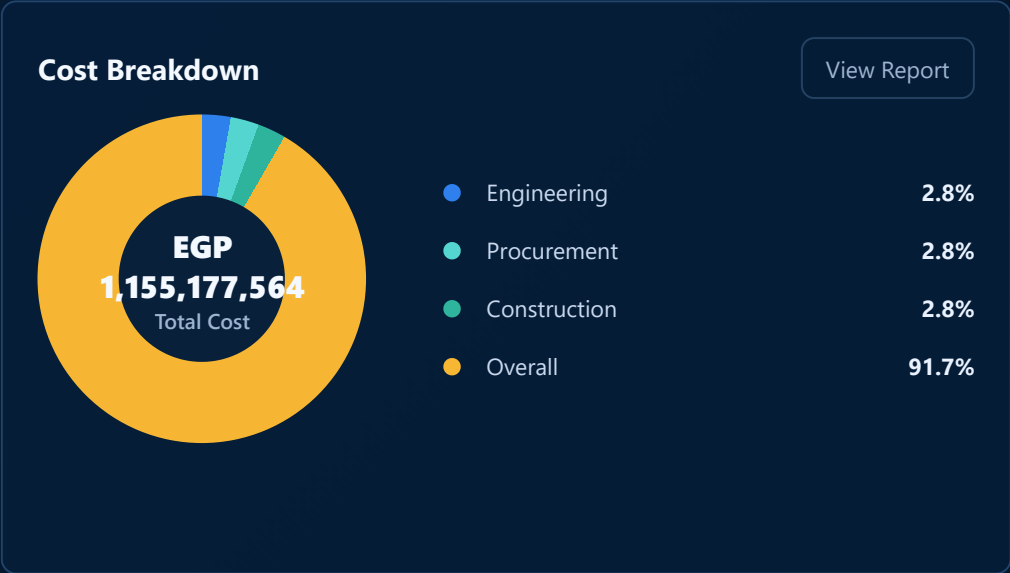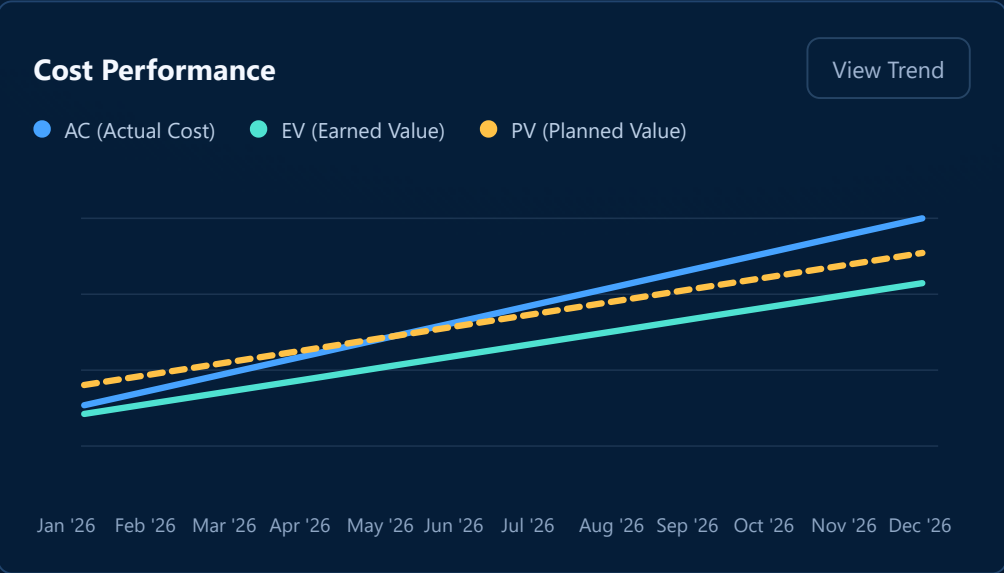

?

Total Activities

17

?

Critical Activities

11

?

SPI

1.05

?

CPI

1.01

?

Active Contracts

2

?

Open RFIs

5

?

Open Submittals

1

