

REPORT DATE: 20-JUL-2026

# Suez Tunnel Civil & MEP Works

This linked executive dashboard is generated from the platform CSV files and updates each time the platform data changes.

Schedule Health

**SPI 0.86**

Contractual Completion

**28-Feb-2027**

Forecast Completion

**18-May-2027**

CONTRACT VALUE

**1,250,000,000  
EGP**

Original contract value

SCHEDULE VARIANCE

**-77,831,325 EGP**

EV minus PV exposure

CUMULATIVE PAID

**481,550,000 EGP**

Paid to date

ONGOING RISKS

**4**

Active project constraints

PROGRESS INTELLIGENCE

## Planned vs Actual by Phase

Planned vs Actual by Phase

40





#### COMMAND DECISIONS

## Critical Recovery Agenda

### Schedule

Ongoing

Steel delivery delay

Impact: High

### Engineering

Ongoing

Late design clarification and IFC revisions

Impact: Medium

### Commercial

Monitoring

Cashflow pressure due to delayed certification

Impact: Medium

### Access constraint and traffic diversion

Ongoing

Access constraint and traffic diversion

Impact: Critical

### MEP sleeve coordination delay

Ongoing

MEP sleeve coordination delay

Impact: Critical

#### PHASE GAUGES

## Plan vs Actual Snapshot

ENGINEERING

PROCUREMENT

0.74%

Planned 0.90% | Variance -0.16%

0.60%

Planned 0.72% | Variance -0.12%

CONSTRUCTION

0.36%

Planned 0.43% | Variance -0.07%

OVERALL

35.00%

Planned 42.00% | Variance -7.00%

MILESTONE EXPOSURE

Forecast Completion by Discipline / Area

| DISCIPLINE   | PLAN COMPLETION                         | FORECAST COMPLETION                     | VARIANCE DAYS |
|--------------|-----------------------------------------|-----------------------------------------|---------------|
| Engineering  | 07-Dec-2025                             | 27-Dec-2025                             | -20           |
| Procurement  | 27-Dec-2025                             | 16-Jan-2026                             | -20           |
| Construction | 01-Jul-2026                             | 21-Jul-2026                             | -20           |
| B-01         | Forecasted completion date: 07-Dec-2025 | Forecasted completion date: 27-Dec-2025 | 0             |
| B-02         | Forecasted completion date: 27-Dec-2025 | Forecasted completion date: 16-Jan-2026 | 0             |
| B-03         | Forecasted completion date: 01-Jul-2026 | Forecasted completion date: 21-Jul-2026 | 0             |
| B-04         | Forecasted completion date: 07-Dec-2025 | Forecasted completion date: 27-Dec-2025 | 0             |

ENGINEERING DELIVERABLES

Document Submission Control

Civil - Submittals

|       |      |        |
|-------|------|--------|
| Total | Plan | Actual |
| 1     | 0    | 0      |

Civil - Shop Drawings

Total

1

Plan


0

Actual

0

CASHFLOW POSITION

Invoice Conversion Funnel

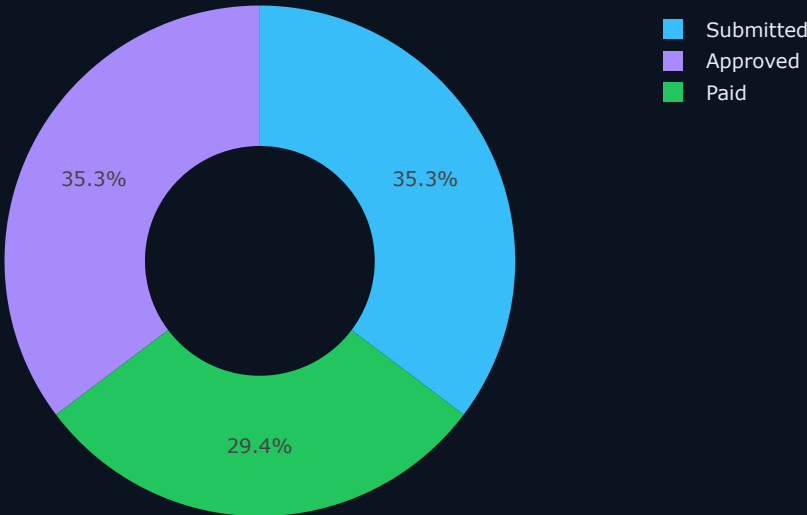

PAID

481,550,000 EGP

Released cash

UNDER PAYMENT

95,950,000 EGP

Certified not yet paid

INVOICES REGISTER


Payment Status Control

| INVOICE    | SUBMISSION DATE | VALUE       | STATUS |
|------------|-----------------|-------------|--------|
| Invoice #1 | 15-Dec-2025     | 58,750,000  | Paid   |
| Invoice #2 | 14-Jan-2026     | 73,750,000  | Paid   |
| Invoice #3 | 13-Feb-2026     | 88,750,000  | Paid   |
| Invoice #4 | 15-Mar-2026     | 103,750,000 | Paid   |

| INVOICE    | SUBMISSION DATE | VALUE       | STATUS         |
|------------|-----------------|-------------|----------------|
| Invoice #5 | 14-Apr-2026     | 118,750,000 | Partially Paid |
| Invoice #6 | 14-May-2026     | 133,750,000 | Certified      |

EARNED VALUE MANAGEMENT

BAC / PV / EV / SV Executive Readout

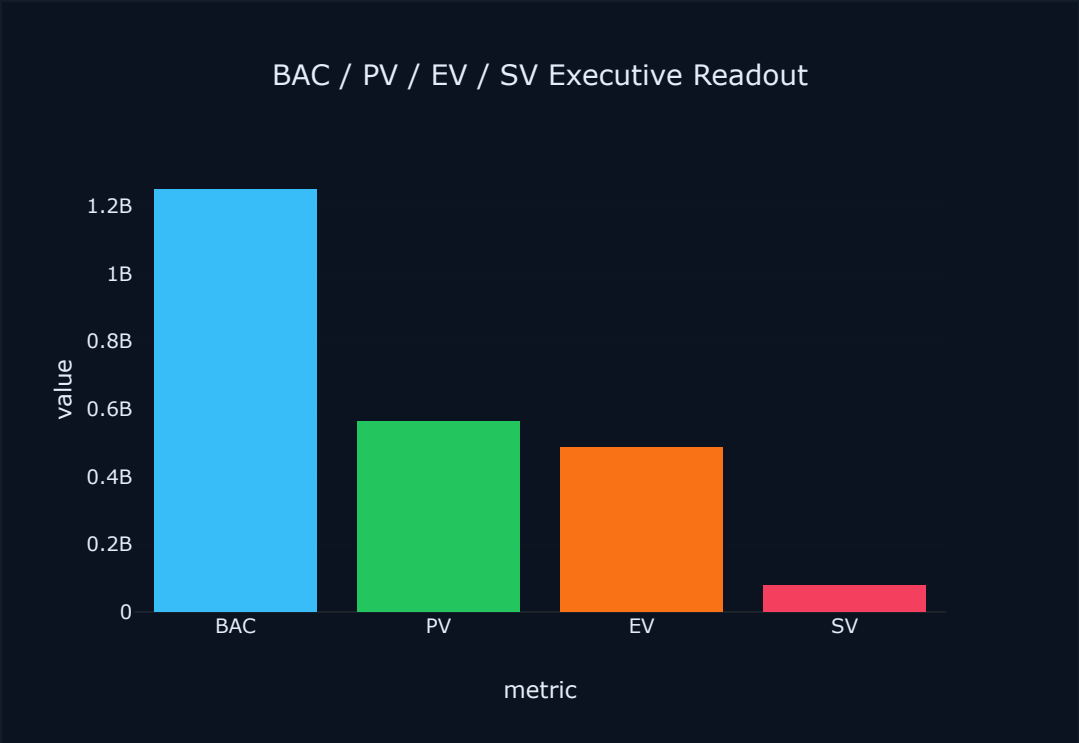

EARNED VALUE ANALYSIS ADD-ON

Quantitative Performance (EVM Metrics)

CRITICAL DELAY

BAC

SAR  
1,249,999,999.99

Budget @ Completion

PV

SAR  
563,253,012.03

Cumm. Planned Value

EV

SV

**SAR**

**485,421,686.74**

Cumm. Earned Value

**SAR**

**-77,831,325.29**

Negative schedule exposure

SPI

**0.86**

Schedule performance index

PLANNED COMPLETION VALUE POSITION

**45.1%**

PV as a share of BAC

EARNED VALUE GAP

**SAR**

**77,831,325.29**


PV not converted into EV

SCHEDULE HEALTH CLASSIFICATION

**Critical Delay**

Executive status

BAC vs PV vs EV with SV Exposure

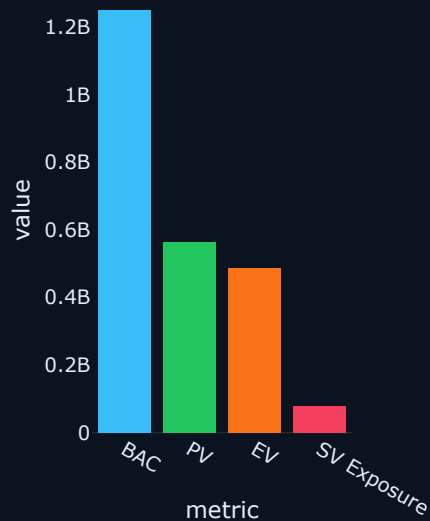

The project is underperforming against the planned value baseline. The earned value is significantly below the planned value, creating a negative schedule variance of SAR 77.83M and an SPI of 0.86. This indicates that the project is progressing at approximately 86% of the planned schedule efficiency.

[ADD / EDIT MY COMMENT](#)

No user comment added.

EARNED VALUE ANALYSIS ADD-ON

Root Cause Linkage

| Cause Title                                                  | Impact Area                              | Link to EVM Impact                                                                                                    | Status  | Severity |
|--------------------------------------------------------------|------------------------------------------|-----------------------------------------------------------------------------------------------------------------------|---------|----------|
| Delay in RFT steel supply by Owner                           | Procurement / Construction               | PV not converted into EV due to blocked work fronts and delayed material-driven execution.                            | Ongoing | Critical |
| Delay in design review process                               | Engineering                              | Planned engineering progress could not flow into approved deliverables and downstream earned value.                   | Closed  | High     |
| Delay in reply on RFI 4 and RFI 5                            | Engineering / Construction               | Technical closure delays restricted workforce release and slowed conversion of planned progress into earned progress. | Ongoing | High     |
| Delay in determining the MEP executing party                 | Engineering / Procurement / Construction | Interface uncertainty delayed execution planning, procurement flow, and forecast progress realization.                | Closed  | Medium   |
| Payment delay impact on resource continuity and productivity | Commercial / Construction                | Liquidity pressure reduced productivity continuity and slowed the conversion of planned value into earned value.      | Closed  | High     |

The negative schedule variance is not an isolated numerical deviation. It is directly linked to unresolved external and interface-driven constraints that prevented planned progress from being converted into earned value, mainly within construction and procurement work fronts.

ADD / EDIT MY COMMENT

No user comment added.

EARNED VALUE ANALYSIS ADD-ON

Contractor Mitigation & Recovery Status

| Action                    | Owner / Responsible Party                        | Current Status | Recovery Impact                                                                     | Required Next Decision                                           |
|---------------------------|--------------------------------------------------|----------------|-------------------------------------------------------------------------------------|------------------------------------------------------------------|
| RFT Steel Supply Recovery | Project Controls / Procurement / Owner Interface | In Progress    | Releases blocked structural work fronts and supports EV generation in construction. | Secure committed steel release and delivery sequence from Owner. |

| ACTION                             | OWNER / RESPONSIBLE PARTY               | CURRENT STATUS                | RECOVERY IMPACT                                                               | REQUIRED NEXT DECISION                                                  |
|------------------------------------|-----------------------------------------|-------------------------------|-------------------------------------------------------------------------------|-------------------------------------------------------------------------|
| RFI Closure Acceleration           | Engineering Team / Consultant Interface | In Progress                   | Enables technical closure and unblocks affected planned activities.           | Escalate overdue RFI responses for closure dates.                       |
| Design Review Follow-up            | Engineering Management                  | Monitoring                    | Protects planned engineering completion and downstream procurement readiness. | Freeze review turnaround commitments with reviewing parties.            |
| MEP Interface Finalization         | Project Management / Client Interface   | Monitoring                    | Reduces interface uncertainty and improves forecast execution reliability.    | Confirm final executing responsibility and interface release logic.     |
| Commercial / Payment Follow-up     | Commercial Team                         | In Progress                   | Supports resource continuity and mitigates productivity disruption risk.      | Close outstanding payment approvals and release under-payment invoices. |
| Construction Productivity Recovery | Construction Team                       | Ready Upon Constraint Removal | Accelerates EV generation once technical and supply constraints are removed.  | Approve recovery sequence by priority work front.                       |

Contractor mitigation is focused on protecting available work fronts, accelerating technical closures, maintaining commercial entitlement records, and recovering productivity once external constraints are removed. Recovery remains dependent on timely closure of outstanding Owner / Engineer-driven constraints.

[ADD](#) / [EDIT MY COMMENT](#)

No user comment added.

#### RISK REGISTER

## Risk & Issue Control

### Schedule

Ongoing

Steel delivery delay

Impact: High

### Engineering

Ongoing

Late design clarification and IFC revisions

Impact: Medium

### Commercial

Monitoring



Cashflow pressure due to delayed certification  
Impact: Medium

Access constraint and traffic diversion

Ongoing

Access constraint and traffic diversion  
Impact: Critical


MEP sleeve coordination delay

Ongoing

MEP sleeve coordination delay  
Impact: Critical

CAUSAL INTELLIGENCE

Root Cause / Impact Radar

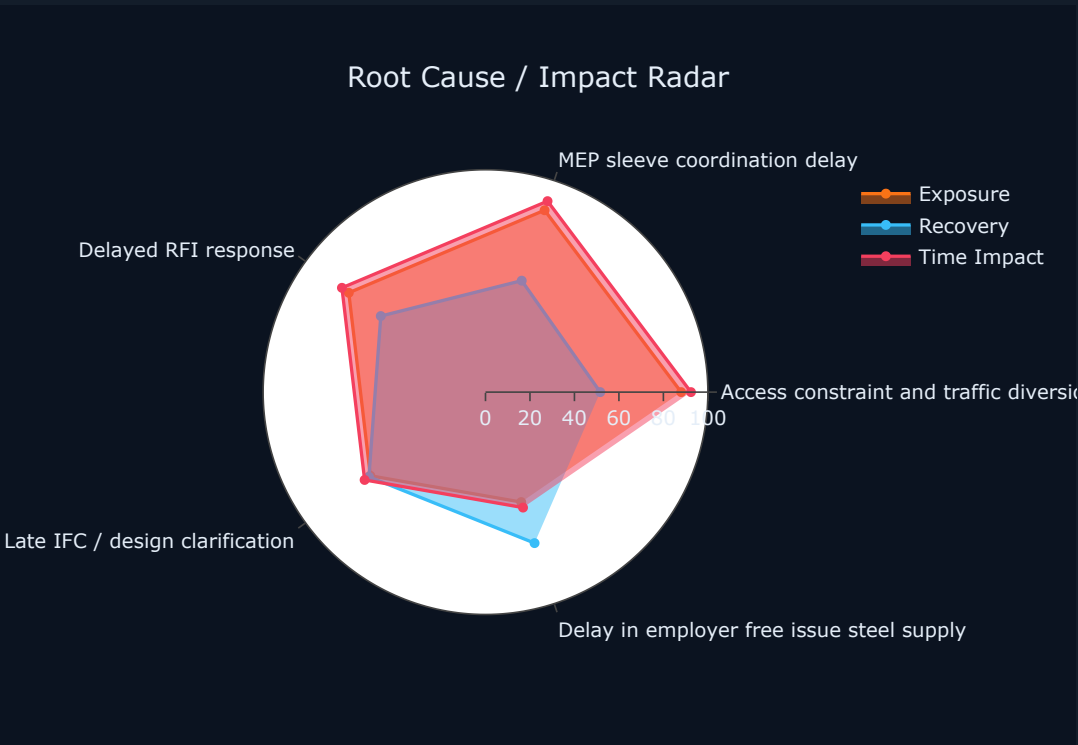

RESOURCE QUANTITIES

RFT Quantity Distribution

No dedicated resource quantity source is currently available.

Effective Date: 01-Sep-2025    Ground Works Forecast: 01-Sep-2025

Strategic priority: recover construction productivity and preserve entitlement evidence.
