

ROYA

EXECUTIVE CONTROL TOWER

REPORT DATE: 20-JUL-2026

ROYA-BIG PROJECT PHASE01 (B1-4)

This linked executive dashboard is generated from the platform CSV files and updates each time the platform data changes.

Schedule Health

SPI 0.45

Contractual Completion

10-Apr-2027

Forecast Completion

19-Aug-2027

CONTRACT VALUE

367,286,025
EGP

Original contract value

SCHEDULE VARIANCE

-139,711,756
EGP

EV minus PV exposure

CUMULATIVE PAID

110,288,532
EGP

Paid to date


ONGOING RISKS

4

Active project constraints

PROGRESS INTELLIGENCE

Planned vs Actual by Phase

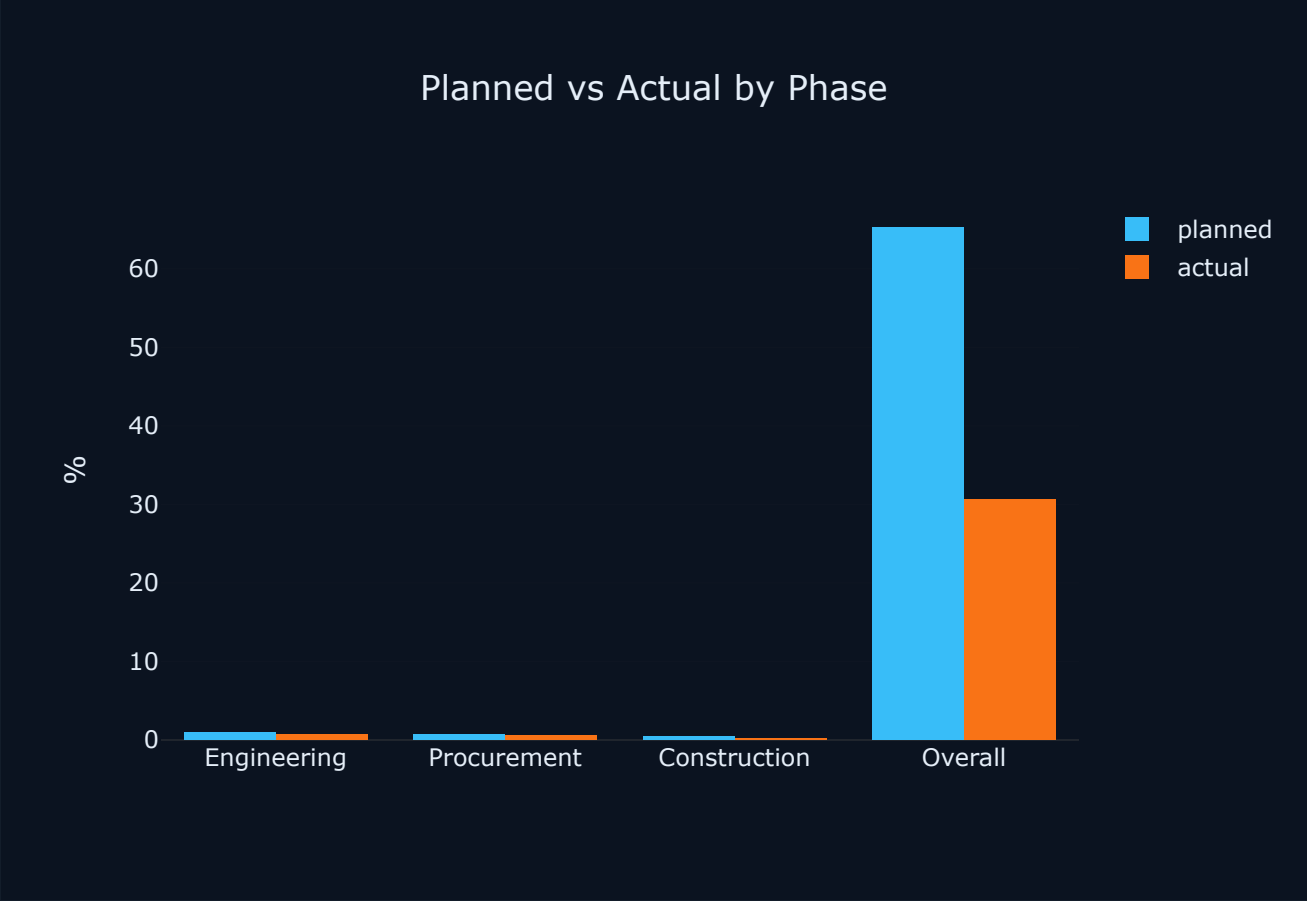

COMMAND DECISIONS

Critical Recovery Agenda

Schedule Steel delivery delay Impact: High	Ongoing
Schedule Deploying MEP sub contractor Impact: High	Closed
IFC IFC	Ongoing

Impact: Critical

IFC

Ongoing

IFC

Impact: Critical

IFC

Ongoing

IFC

Impact: Critical

PHASE GAUGES

Plan vs Actual Snapshot

ENGINEERING

0.64%

Planned 0.98% | Variance -0.35%

PROCUREMENT

0.53%

Planned 0.72% | Variance -0.19%

CONSTRUCTION

0.08%

Planned 0.44% | Variance -0.37%

OVERALL

30.68%

Planned 65.32% | Variance -34.64%

MILESTONE EXPOSURE

Forecast Completion by Discipline / Area

DISCIPLINE	PLAN COMPLETION	FORECAST COMPLETION	VARIANCE DAYS
Engineering	07-Jun-2026	27-Feb-2027	-265
Procurement	16-Jan-2027	02-Sep-2027	-229

DISCIPLINE	PLAN COMPLETION	FORECAST COMPLETION	VARIANCE DAYS
Construction	05-Apr-2027	02-Sep-2027	-150
B-01	05-Apr-2027	05-Apr-2027	0
B-02	23-Mar-2027	02-Sep-2027	-163
B-03	05-Apr-2027	05-Apr-2027	0
B-04	05-Apr-2027	05-Apr-2027	0

ENGINEERING DELIVERABLES

Document Submission Control

Civil - Submittals


Total	Plan	Actual
193	0	0


Civil - Shop Drawings

Total	Plan	Actual
193	0	0

CASHFLOW POSITION

Invoice Conversion Funnel



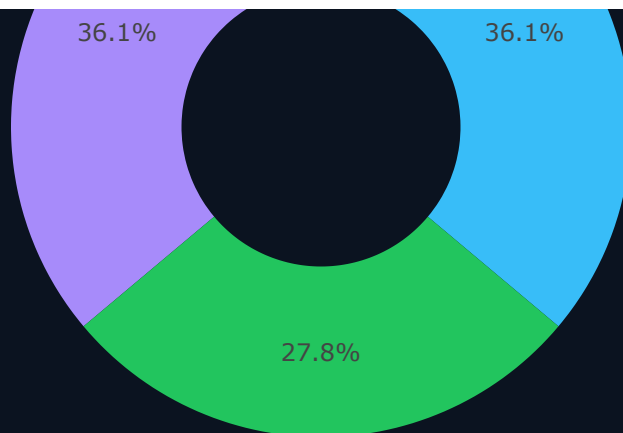

PAID

110,288,532
EGP

Released cash

UNDER PAYMENT

33,117,234
EGP


Certified not yet paid

INVOICES REGISTER

Payment Status Control

INVOICE	SUBMISSION DATE	VALUE	STATUS
Invoice #1	06-Dec-2025	23,485,862	Paid
Invoice #2	29-Dec-2025	26,309,020	Paid
Invoice #3	24-Jan-2026	20,099,944	Paid
Invoice #4	25-Feb-2026	40,393,706	Paid
Invoice #5	25-Mar-2026	17,641,619	Under Payment
Invoice #6	26-Apr-2026	15,475,615	Under Payment

BAC / PV / EV / SV Executive Readout

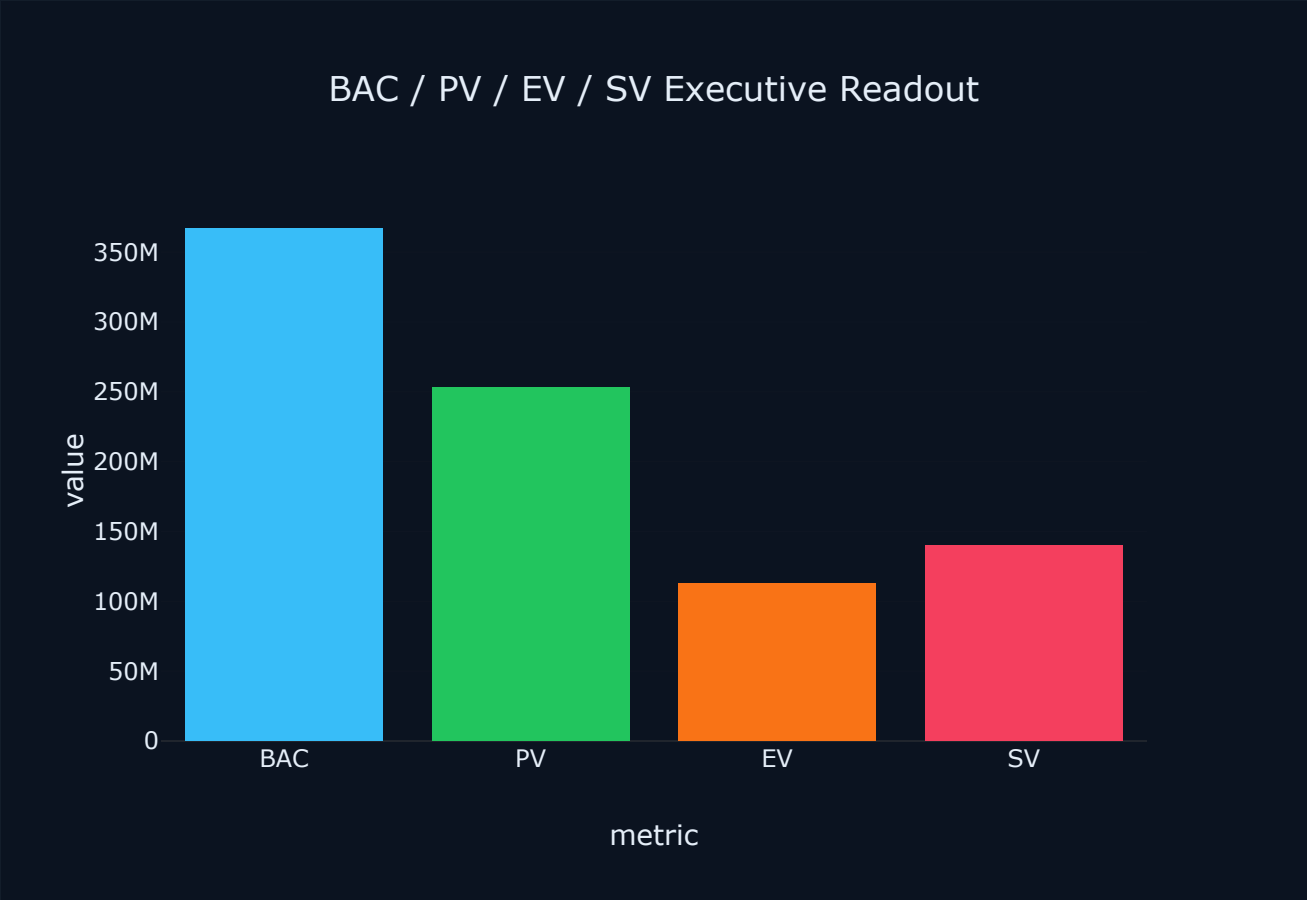

Quantitative Performance (EVM Metrics)

CRITICAL DELAY

BAC

SAR

367,286,024.99

Budget @ Completion

PV

SAR

252,796,791.16

Cumm. Planned Value

EV

SV

SAR

113,085,034.82

Cumm. Earned Value

SAR

-139,711,756.34

Negative schedule exposure

SPI

0.45

Schedule performance index

PLANNED COMPLETION VALUE POSITION

68.8%

PV as a share of BAC

EARNED VALUE GAP

SAR

139,711,756.34


PV not converted into EV

SCHEDULE HEALTH CLASSIFICATION


Critical Delay

Executive status

BAC vs PV vs EV with SV Exposure

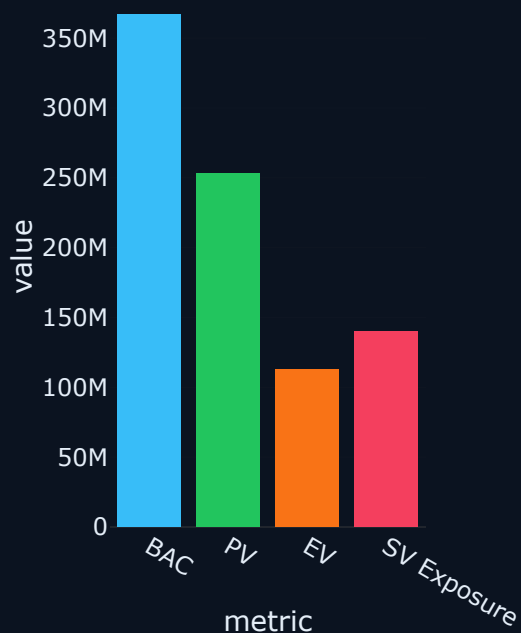

SPI Health

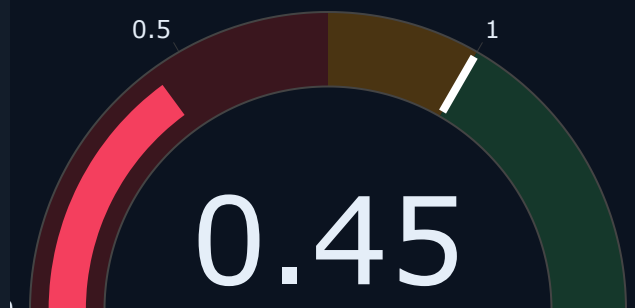

The project is underperforming against the planned value baseline. The earned value is significantly below the planned value, creating a negative schedule variance of SAR 139.71M and an SPI of 0.45. This indicates that the project is progressing at approximately 45% of the planned schedule efficiency.

ADD / EDIT MY COMMENT

No user comment added.

EARNED VALUE ANALYSIS ADD-ON

Root Cause Linkage

CAUSE TITLE	IMPACT AREA	LINK TO EVM IMPACT	STATUS	SEVERITY
Delay in RFT steel supply by Owner	Procurement / Construction	PV not converted into EV due to blocked work fronts and delayed material-driven execution.	Ongoing	Critical
Delay in design review process	Engineering	Planned engineering progress could not flow into approved deliverables and downstream earned value.	Closed	High
Delay in reply on RFI 4 and RFI 5	Engineering / Construction	Technical closure delays restricted workface release and slowed conversion of planned progress into earned progress.	Ongoing	High
Delay in determining the MEP executing party	Engineering / Procurement / Construction	Interface uncertainty delayed execution planning, procurement flow, and forecast progress realization.	Closed	Medium
Payment delay impact on resource continuity and productivity	Commercial / Construction	Liquidity pressure reduced productivity continuity and slowed the conversion of planned value into earned value.	Ongoing	High

The negative schedule variance is not an isolated numerical deviation. It is directly linked to unresolved external and interface-driven constraints that prevented planned progress from being converted into earned value, mainly within construction and procurement work fronts.

ADD / EDIT MY COMMENT

No user comment added.

EARNED VALUE ANALYSIS ADD-ON

Contractor Mitigation & Recovery Status

ACTION	OWNER / RESPONSIBLE PARTY	CURRENT STATUS	RECOVERY IMPACT	REQUIRED NEXT DECISION
RFT Steel Supply Recovery	Project Controls / Procurement / Owner Interface	In Progress	Releases blocked structural work fronts and supports EV generation in construction.	Secure committed steel release and delivery sequence from Owner.
RFI Closure Acceleration	Engineering Team / Consultant Interface	In Progress	Enables technical closure and unblocks affected planned activities.	Escalate overdue RFI responses for closure dates.
Design Review Follow-up	Engineering Management	Monitoring	Protects planned engineering completion and downstream procurement readiness.	Freeze review turnaround commitments with reviewing parties.
MEP Interface Finalization	Project Management / Client Interface	Monitoring	Reduces interface uncertainty and improves forecast execution reliability.	Confirm final executing responsibility and interface release logic.
Commercial / Payment Follow-up	Commercial Team	In Progress	Supports resource continuity and mitigates	Close outstanding payment approvals and

ACTION	OWNER / RESPONSIBLE PARTY	CURRENT STATUS	RECOVERY IMPACT	REQUIRED NEXT DECISION
			productivity disruption risk.	release under-payment invoices.
Construction Productivity Recovery	Construction Team	Ready Upon Constraint Removal	Accelerates EV generation once technical and supply constraints are removed.	Approve recovery sequence by priority work front.

Contractor mitigation is focused on protecting available work fronts, accelerating technical closures, maintaining commercial entitlement records, and recovering productivity once external constraints are removed. Recovery remains dependent on timely closure of outstanding Owner / Engineer-driven constraints.

ADD / EDIT MY COMMENT

No user comment added.

RISK REGISTER

Risk & Issue Control

Schedule

Ongoing

Steel delivery delay

Impact: High

Schedule

Closed

Deploying MEP sub contractor

Impact: High

IFC

Ongoing

IFC

Impact: Critical

IFC

Ongoing

IFC

Impact: Critical

IFC

Ongoing


IFC

Impact: Critical

CAUSAL INTELLIGENCE

Root Cause / Impact Radar

Root Cause / Impact Radar

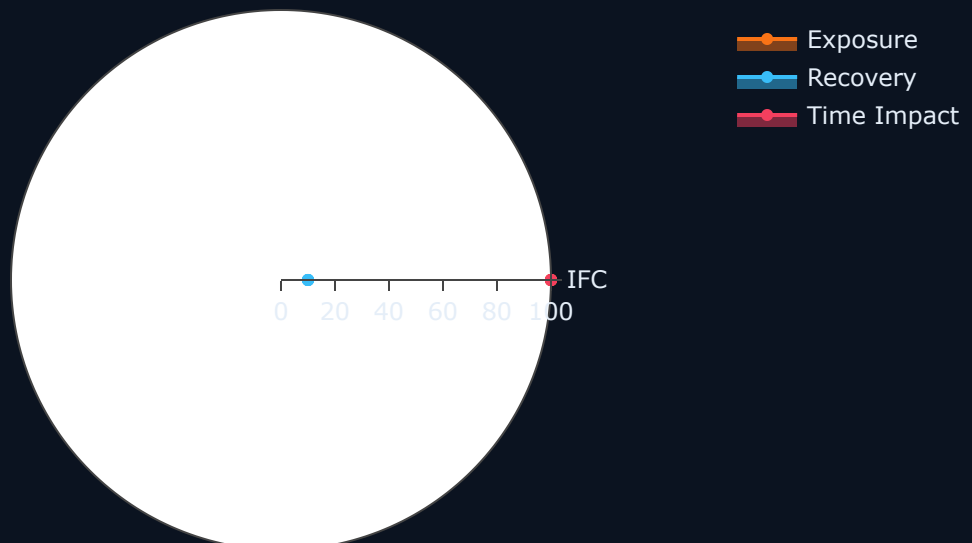

RESOURCE QUANTITIES

RFT Quantity Distribution

No dedicated resource quantity source is currently available.

Effective Date: 11-Sep-2025 Æ'çâ,¬Å;fâ€šÃ,Â· Ground Works Forecast: 11-Sep-2025

Strategic priority: recover construction productivity and preserve entitlement evidence.
