

# Sophia Mall Mixed-Use Development

This linked executive dashboard is generated from the platform CSV files and updates each time the platform data changes.

Schedule Health

**SPI 1.05**

Contractual Completion

**31-Jul-2027**

Forecast Completion

**25-Aug-2027**

CONTRACT VALUE

**2,100,000,000  
EGP**

Original contract value

SCHEDULE VARIANCE

**54,352,048 EGP**

EV minus PV exposure

CUMULATIVE PAID

**809,004,000 EGP**

Paid to date


ONGOING RISKS

**4**

Active project constraints

PROGRESS INTELLIGENCE

## Planned vs Actual by Phase



COMMAND DECISIONS

## Critical Recovery Agenda

Schedule

Steel delivery delay

Ongoing

Impact: Medium

Engineering

Ongoing

Late design clarification and IFC revisions

Impact: Medium

Commercial

Monitoring

Cashflow pressure due to delayed certification

Impact: Medium

Access constraint and traffic diversion

Ongoing

Access constraint and traffic diversion

Impact: Critical

MEP sleeve coordination delay

Ongoing

MEP sleeve coordination delay

Impact: Critical

PHASE GAUGES

Plan vs Actual Snapshot

ENGINEERING

0.89%

Planned 0.84% | Variance 0.05%

PROCUREMENT

0.71%

Planned 0.67% | Variance 0.04%

CONSTRUCTION

0.60%

Planned 0.57% | Variance 0.03%

OVERALL

33.00%

Planned 31.00% | Variance 2.00%

MILESTONE EXPOSURE

Forecast Completion by Discipline / Area

| DISCIPLINE   | PLAN COMPLETION                       | FORECAST COMPLETION                   | VARIANCE DAYS |  |
|--------------|---------------------------------------|---------------------------------------|---------------|--|
| Engineering  | 10-Feb-2026                           | 12-Feb-2026                           | -2            |  |
| Procurement  | 02-Mar-2026                           | 04-Mar-2026                           | -2            |  |
| Construction | 04-Sep-2026                           | 06-Sep-2026                           | -2            |  |
| B-01         | ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□ | ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□ | 0             |  |
| B-02         | ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□ | ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□ | 0             |  |
| B-03         | ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□ | ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□ | 0             |  |
| B-04         | ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□ | ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□ | 0             |  |

ENGINEERING DELIVERABLES

Document Submission Control

Civil - Submittals

|       |      |        |
|-------|------|--------|
| Total | Plan | Actual |
| 1     | 0    | 0      |

Civil - Shop Drawings

|       |      |        |
|-------|------|--------|
| Total | Plan | Actual |
| 1     | 0    | 0      |

CASHFLOW POSITION

Invoice Conversion Funnel



INVOICES REGISTER

Payment Status Control

| INVOICE PAID    | SUBMISSION DATE | VALUE UNDER PAYMENT    | STATUS         |
|-----------------|-----------------|------------------------|----------------|
| Invoice #1      | 28-Jun-2025     | 88,900,000             | Paid           |
| 809,004,000 EGP |                 | 161,196,000 EGP        |                |
| Invoice #2      | 27-Feb-2026     | 123,900,000            | Paid           |
| Released cash   |                 | Certified not yet paid |                |
| Invoice #3      | 29-Mar-2026     | 149,100,000            | Paid           |
| Invoice #4      | 28-Apr-2026     | 174,300,000            | Paid           |
| Invoice #5      | 28-May-2026     | 199,500,000            | Partially Paid |
| Invoice #6      | 27-Jun-2026     | 224,700,000            | Certified      |

#### EARNED VALUE MANAGEMENT

### BAC / PV / EV / SV Executive Readout



#### EARNED VALUE ANALYSIS ADD-ON

### Quantitative Performance (EVM Metrics)

STABLE

BAC

**SAR**  
**2,100,000,000.01**

Budget @ Completion

PV

**SAR**  
**1,112,493,975.91**

Cumm. Planned Value

EV

**SAR**  
**1,166,846,024.09**

Cumm. Earned Value

SV

**SAR**  
**54,352,048.18**

Negative schedule exposure

SPI

**1.05**

PLANNED COMPLETION VALUE POSITION

**53.0%**

Schedule performance index

PV as a share of BAC

EARNED VALUE GAP

**SAR**  
**-54,352,048.18**



PV not converted into EV

SCHEDULE HEALTH CLASSIFICATION

**Stable**

Executive status

BAC vs PV vs EV with SV Exposure

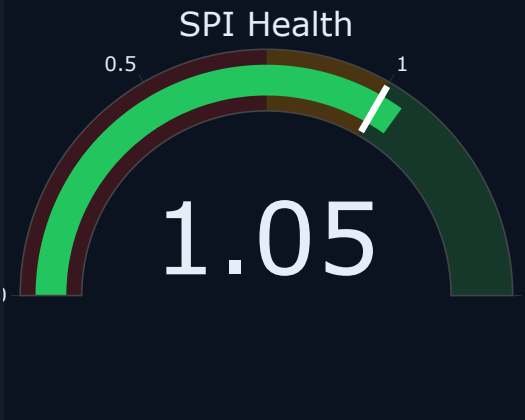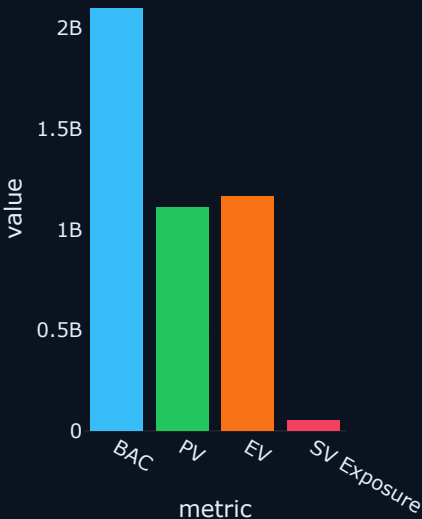

The project is underperforming against the planned value baseline. The earned value is significantly below the planned value, creating a negative schedule variance of SAR 54.35M and an SPI of 1.05. This indicates that the project is progressing at approximately 105% of the planned schedule efficiency.

**ADD / EDIT MY COMMENT**

No user comment added.

EARNED VALUE ANALYSIS ADD-ON

**Root Cause Linkage**

| Cause Title                                                  | Impact Area                              | Link to EVM Impact                                                                                                    | Status  | Severity |
|--------------------------------------------------------------|------------------------------------------|-----------------------------------------------------------------------------------------------------------------------|---------|----------|
| Delay in RFT steel supply by Owner                           | Procurement / Construction               | PV not converted into EV due to blocked work fronts and delayed material-driven execution.                            | Ongoing | Critical |
| Delay in design review process                               | Engineering                              | Planned engineering progress could not flow into approved deliverables and downstream earned value.                   | Closed  | High     |
| Delay in reply on RFI 4 and RFI 5                            | Engineering / Construction               | Technical closure delays restricted workforce release and slowed conversion of planned progress into earned progress. | Ongoing | High     |
| Delay in determining the MEP executing party                 | Engineering / Procurement / Construction | Interface uncertainty delayed execution planning, procurement flow, and forecast progress realization.                | Closed  | Medium   |
| Payment delay impact on resource continuity and productivity | Commercial / Construction                | Liquidity pressure reduced productivity continuity and slowed the conversion of planned value into earned value.      | Closed  | High     |

The negative schedule variance is not an isolated numerical deviation. It is directly linked to unresolved external and interface-driven constraints that prevented planned progress from being converted into earned value, mainly within construction and procurement work fronts.

ADD / EDIT MY COMMENT

No user comment added.

EARNED VALUE ANALYSIS ADD-ON

Contractor Mitigation & Recovery Status

| Action                     | Owner / Responsible Party                        | Current Status | Recovery Impact                                                                     | Required Next Decision                                              |
|----------------------------|--------------------------------------------------|----------------|-------------------------------------------------------------------------------------|---------------------------------------------------------------------|
| RFT Steel Supply Recovery  | Project Controls / Procurement / Owner Interface | In Progress    | Releases blocked structural work fronts and supports EV generation in construction. | Secure committed steel release and delivery sequence from Owner.    |
| RFI Closure Acceleration   | Engineering Team / Consultant Interface          | In Progress    | Enables technical closure and unblocks affected planned activities.                 | Escalate overdue RFI responses for closure dates.                   |
| Design Review Follow-up    | Engineering Management                           | Monitoring     | Protects planned engineering completion and downstream procurement readiness.       | Freeze review turnaround commitments with reviewing parties.        |
| MEP Interface Finalization | Project Management / Client Interface            | Monitoring     | Reduces interface uncertainty and improves                                          | Confirm final executing responsibility and interface release logic. |

| ACTION                             | OWNER / RESPONSIBLE PARTY | CURRENT STATUS                | RECOVERY IMPACT                                                              | REQUIRED NEXT DECISION                                                  |
|------------------------------------|---------------------------|-------------------------------|------------------------------------------------------------------------------|-------------------------------------------------------------------------|
|                                    |                           |                               | forecast execution reliability.                                              |                                                                         |
| Commercial / Payment Follow-up     | Commercial Team           | In Progress                   | Supports resource continuity and mitigates productivity disruption risk.     | Close outstanding payment approvals and release under-payment invoices. |
| Construction Productivity Recovery | Construction Team         | Ready Upon Constraint Removal | Accelerates EV generation once technical and supply constraints are removed. | Approve recovery sequence by priority work front.                       |

Contractor mitigation is focused on protecting available work fronts, accelerating technical closures, maintaining commercial entitlement records, and recovering productivity once external constraints are removed. Recovery remains dependent on timely closure of outstanding Owner / Engineer-driven constraints.

**ADD / EDIT MY COMMENT**

No user comment added.

#### RISK REGISTER

## Risk & Issue Control

### Schedule

Ongoing

Steel delivery delay

Impact: Medium

### Engineering

Ongoing

Late design clarification and IFC revisions

Impact: Medium

### Commercial

Monitoring

Cashflow pressure due to delayed certification

Impact: Medium

### Access constraint and traffic diversion

Ongoing

Access constraint and traffic diversion

Impact: Critical

MEP sleeve coordination delay


Ongoing

MEP sleeve coordination delay

Impact: Critical

CAUSAL INTELLIGENCE

Root Cause / Impact Radar



RFT Quantity Distribution

No dedicated resource quantity source is currently available.

Effective Date: 15-Oct-2025 - Ground Works Forecast: 15-Oct-2025

Strategic priority: recover construction productivity and preserve entitlement evidence.
