

SUEZ URBAN DEVELOPMENT AUTHORITY

EXECUTIVE CONTROL TOWER

REPORT DATE: 01-AUG-2026

Suez Tunnel Civil & MEP Works

This linked executive dashboard is generated from the platform CSV files and updates each time the platform data changes.

Schedule Health

SPI 0.86

Contractual Completion

28-Feb-2027

Forecast Completion

18-May-2027

CONTRACT VALUE

**1,250,000,000
EGP**

Original contract value

SCHEDULE VARIANCE

-77,831,325 EGP

EV minus PV exposure

CUMULATIVE PAID

481,550,000 EGP

Paid to date

ONGOING RISKS

4

Active project constraints

PROGRESS INTELLIGENCE

Planned vs Actual by Phase

20

Engineering

Procurement

Construction

Overall

planned

COMMAND DECISIONS

Critical Recovery Agenda

Schedule

Ongoing

Steel delivery delay

Impact: High

Engineering

Ongoing

Late design clarification and IFC revisions

Impact: Medium

Commercial

Monitoring

Cashflow pressure due to delayed certification

Impact: Medium

Access constraint and traffic diversion

Ongoing

Access constraint and traffic diversion

Impact: Critical

MEP sleeve coordination delay

Ongoing

MEP sleeve coordination delay

Impact: Critical

PHASE GAUGES

Plan vs Actual Snapshot

ENGINEERING

0.74%

Planned 0.90% | Variance -0.16%

PROCUREMENT

0.60%

Planned 0.72% | Variance -0.12%

CONSTRUCTION

0.36%

Planned 0.43% | Variance -0.07%

OVERALL

35.00%

Planned 42.00% | Variance -7.00%

MILESTONE EXPOSURE

Forecast Completion by Discipline / Area

DISCIPLINE	PLAN COMPLETION	FORECAST COMPLETION	VARIANCE DAYS	
Engineering	07-Dec-2025	27-Dec-2025	-20	
Procurement	27-Dec-2025	16-Jan-2026	-20	
Construction	01-Jul-2026	21-Jul-2026	-20	
B-01	ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□	ÅfÆ'Å,ÅçÅfÅçÃçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□	0	
B-02	ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□	ÅfÆ'Å,ÅçÅfÅçÃçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□	0	
B-03	ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□	ÅfÆ'Å,ÅçÅfÅçÃçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□	0	
B-04	ÅfÆ'Å,ÅçÅfÅçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□	ÅfÆ'Å,ÅçÅfÅçÃçÃçâ,¬Å¡Å,Å¬ÅfÅçÃçâ€Å¬Å,Å□	0	

ENGINEERING DELIVERABLES

Document Submission Control

Civil - Submittals

Total	Plan	Actual
1	0	0

Civil - Shop Drawings

Total	Plan	Actual
1	0	0

CASHFLOW POSITION

Invoice Conversion Funnel



INVOICES REGISTER

Payment Status Control

INVOICE PAID	SUBMISSION DATE	VALUE UNDER PAYMENT	STATUS
Invoice #1 Released cash	15-Jan-2026	88,750,000	Paid
Invoice #2 Released cash	14-Jan-2026	73,750,000	Paid
Invoice #3	13-Feb-2026	88,750,000	Paid
Invoice #4	15-Mar-2026	103,750,000	Paid
Invoice #5	14-Apr-2026	118,750,000	Partially Paid
Invoice #6	14-May-2026	133,750,000	Certified

EARNED VALUE MANAGEMENT

BAC / PV / EV / SV Executive Readout



EARNED VALUE ANALYSIS ADD-ON

Quantitative Performance (EVM Metrics)

CRITICAL DELAY

BAC

SAR
1,249,999,999.99

Budget @ Completion

PV

SAR
563,253,012.03

Cumm. Planned Value

EV

SAR
485,421,686.74

Cumm. Earned Value

SV

SAR
-77,831,325.29

Negative schedule exposure

SPI

0.86

PLANNED COMPLETION VALUE POSITION

45.1%

Schedule performance index

PV as a share of BAC

EARNED VALUE GAP

SAR

77,831,325.29


PV not converted into EV

SCHEDULE HEALTH CLASSIFICATION

Critical Delay

Executive status

BAC vs PV vs EV with SV Exposure

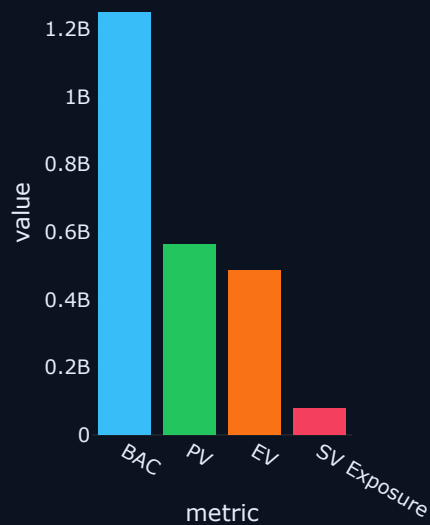

The project is underperforming against the planned value baseline. The earned value is significantly below the planned value, creating a negative schedule variance of SAR 77.83M and an SPI of 0.86. This indicates that the project is progressing at approximately 86% of the planned schedule efficiency.

ADD / EDIT MY COMMENT

No user comment added.

EARNED VALUE ANALYSIS ADD-ON

Root Cause Linkage

Cause Title	Impact Area	Link to EVM Impact	Status	Severity
Delay in RFT steel supply by Owner	Procurement / Construction	PV not converted into EV due to blocked work fronts and delayed material-driven execution.	Ongoing	Critical
Delay in design review process	Engineering	Planned engineering progress could not flow into approved deliverables and downstream earned value.	Closed	High
Delay in reply on RFI 4 and RFI 5	Engineering / Construction	Technical closure delays restricted workforce release and slowed conversion of planned progress into earned progress.	Ongoing	High
Delay in determining the MEP executing party	Engineering / Procurement / Construction	Interface uncertainty delayed execution planning, procurement flow, and forecast progress realization.	Closed	Medium
Payment delay impact on resource continuity and productivity	Commercial / Construction	Liquidity pressure reduced productivity continuity and slowed the conversion of planned value into earned value.	Closed	High

The negative schedule variance is not an isolated numerical deviation. It is directly linked to unresolved external and interface-driven constraints that prevented planned progress from being converted into earned value, mainly within construction and procurement work fronts.

ADD / EDIT MY COMMENT

No user comment added.

EARNED VALUE ANALYSIS ADD-ON

Contractor Mitigation & Recovery Status

Action	Owner / Responsible Party	Current Status	Recovery Impact	Required Next Decision
RFT Steel Supply Recovery	Project Controls / Procurement / Owner Interface	In Progress	Releases blocked structural work fronts and supports EV generation in construction.	Secure committed steel release and delivery sequence from Owner.
RFI Closure Acceleration	Engineering Team / Consultant Interface	In Progress	Enables technical closure and unblocks affected planned activities.	Escalate overdue RFI responses for closure dates.
Design Review Follow-up	Engineering Management	Monitoring	Protects planned engineering completion and downstream procurement readiness.	Freeze review turnaround commitments with reviewing parties.
MEP Interface Finalization	Project Management / Client Interface	Monitoring	Reduces interface uncertainty and improves	Confirm final executing responsibility and interface release logic.

ACTION	OWNER / RESPONSIBLE PARTY	CURRENT STATUS	RECOVERY IMPACT	REQUIRED NEXT DECISION
			forecast execution reliability.	
Commercial / Payment Follow-up	Commercial Team	In Progress	Supports resource continuity and mitigates productivity disruption risk.	Close outstanding payment approvals and release under-payment invoices.
Construction Productivity Recovery	Construction Team	Ready Upon Constraint Removal	Accelerates EV generation once technical and supply constraints are removed.	Approve recovery sequence by priority work front.

Contractor mitigation is focused on protecting available work fronts, accelerating technical closures, maintaining commercial entitlement records, and recovering productivity once external constraints are removed. Recovery remains dependent on timely closure of outstanding Owner / Engineer-driven constraints.

ADD / EDIT MY COMMENT

No user comment added.

RISK REGISTER

Risk & Issue Control

Schedule

Ongoing

Steel delivery delay

Impact: High

Engineering

Ongoing

Late design clarification and IFC revisions

Impact: Medium

Commercial

Monitoring

Cashflow pressure due to delayed certification

Impact: Medium

Access constraint and traffic diversion

Ongoing

Access constraint and traffic diversion

Impact: Critical

MEP sleeve coordination delay


Ongoing

MEP sleeve coordination delay

Impact: Critical

CAUSAL INTELLIGENCE

Root Cause / Impact Radar



RESOURCE QUANTITIES

RFT Quantity Distribution

No dedicated resource quantity source is currently available.

Effective Date: 01-Sep-2025 Effective Date: 01-Sep-2025 Ground Works Forecast: 01-Sep-2025

Strategic priority: recover construction productivity and preserve entitlement evidence.
