

Executive Dashboard

Project Performance & Control Center

01 Aug 2026

Good Morning,
Executive Director

?

Earned Value Management

?

BAC

EGP

367,286,025

Budget at Completion

?

AC

EGP

113,085,035

Actual Cost

?

EV

EGP

113,085,035

Earned Value

?

PV

EGP

252,796,791

Planned Value

?

Schedule Variance

EGP

-139,711,756

Behind Schedule

?

Cost Variance

EGP 0

Under Budget

?

EAC

EGP

367,286,025

Estimate at Completion

?

TCPI

1.000

To Complete Performance Index

Critical Alerts

View All

!

Steel Supply Delay

Delay in steel shipment affecting structure building progress

High

!

IFC Clash Detected

16 clashes found in current coordination records

High

?

RFIs Pending

4 RFIs are pending response from consultants

Medium

?

Contract Exposure

Exposure amount exceeds threshold for active contracts

Medium

Performance Overview

Overall Progress

30.7%

Actual Complete

Planned Progress

65.3%

Baseline Plan

?

Contract Value

EGP

367,286,025

Total Contract Value

?

Actual Cost

EGP




113,085,035

30.8% of BAC

Remaining Duration

43.8%

252 Days Left

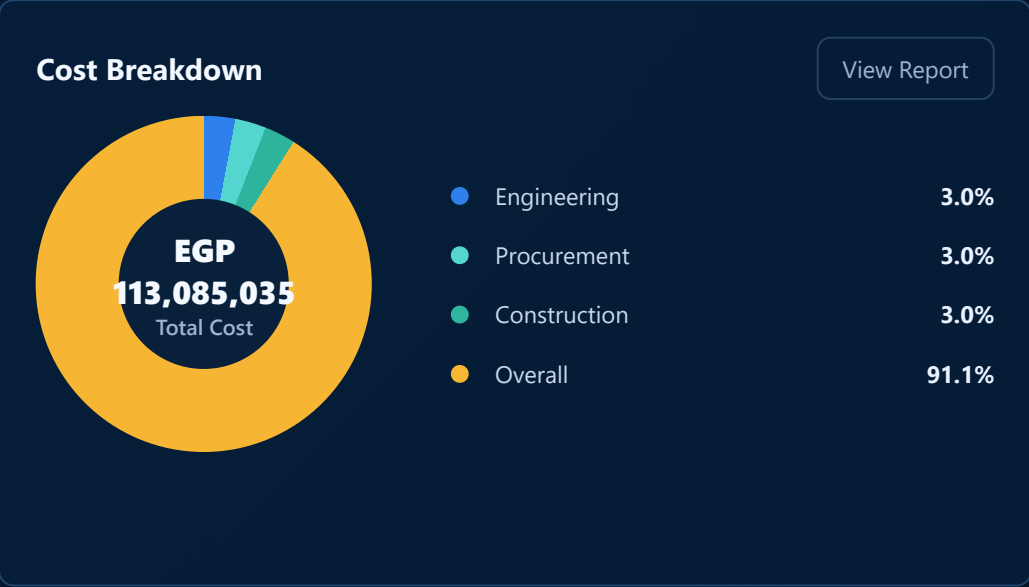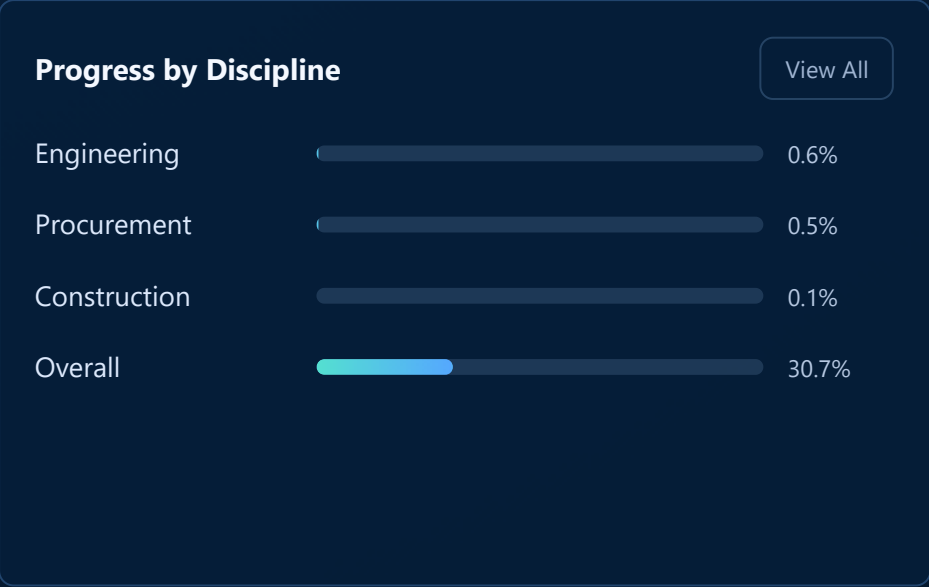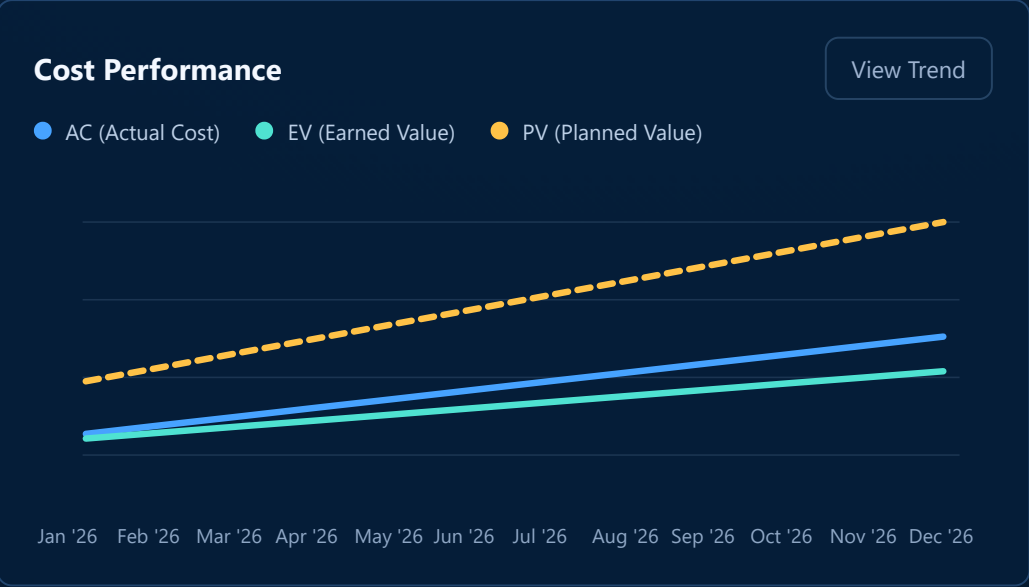

?

Total Activities

1,363

?

Critical Activities

573

?

SPI

0.45

?

CPI

1.00

?

Active Contracts

2

?

Open RFIs

4

?

Open Submittals

791

SAMCO

ROYA-BIG PROJECT PHASE01 (B1-4)

